

Date : 09/05/2025
Project No : 2025C146
Client Company : Davidson Homes, LLC
Arrival Time : 09/05/2025 10:00
Onsite Hours : 04:45


ASEC Report ID : 85178
Name of the Project : Greene Farms Subdivision
Project Location : 1451 Highway 113, Cartersville, Georgia
Weather : N/A
Departure Time : 09/05/2025 14:45
ASEC Technician Name : Solomon Cherie

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Our ASEC representative was on site as requested and observed the grading contractor continue placing fill for the building pads and roadway. Backfilling was to continue today but in-situ soils were found to be too wet. Contractor scarified wet soils to aerate and will recompact tomorrow.

Today, the lots whose moisture and compaction tests failed yesterday was scarified and recompact. Lot retests whose tests for moisture and compaction failed yesterday met job specifications for compaction. A verifying check plug was performed. Density tests were performed using a Troxler nuclear gauge model 3430, serial no. 38069. Results are attached.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

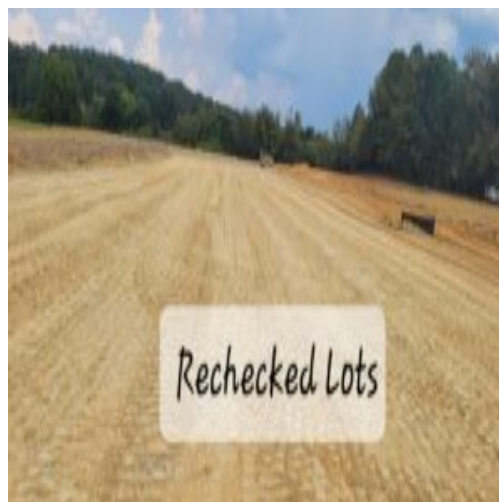

Picture depicting lots#53-58 were rechecked and passed after scarifying

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without

Date : 09/05/2025
Project No : 2025C146
Client Company : Davidson Homes, LLC
Arrival Time : 09/05/2025 10:00
Onsite Hours : 04:45

ASEC Report ID : 85178
Name of the Project : Greene Farms Subdivision
Project Location : 1451 Highway 113, Cartersville, Georgia
Weather : N/A
Departure Time : 09/05/2025 14:45
ASEC Technician Name : Solomon Cherie

written approval from AS Engineering and Consulting LLC.
