

Date : 03/27/2026
Project No : 2025C149
Client Company : Davidson Homes
Arrival Time : 03/27/2026 08:00
Onsite Hours : 06:00

ASEC Report ID : 92034
Name of the Project : Grove at E. Thompson Mill Rd
Project Location : Buford
Weather : sunny
Departure Time : 03/27/2026 14:00
ASEC Technician Name : Samara Simha Reddy Kandi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Crew continued earthwork operations on Lots #6 and 48. Backfill material was placed in lifts of approximately 6-8 inches thickness and spread evenly using a crawler bulldozer. Each lift was compacted using both a sheep-foot roller and a Caterpillar 815 compactor. Results of compaction testing were reported to the contractor.


In the neighboring Buford area, the crew excavated a trench to the required depth and prepared the base for pipe installation. No. 57 stone was placed to provide a stable bedding layer. Following this, an approximately 11-foot-long ductile iron pipe (DIP) was installed and connected to the previously installed pipe. Additional No. 57 stone was then placed around the pipe prior further backfilling activities.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you



Date : 03/27/2026
Project No : 2025C149
Client Company : Davidson Homes
Arrival Time : 03/27/2026 08:00
Onsite Hours : 06:00

ASEC Report ID : 92034
Name of the Project : Grove at E. Thompson Mill Rd
Project Location : Buford
Weather : sunny
Departure Time : 03/27/2026 14:00
ASEC Technician Name : Samara Simha Reddy Kandi

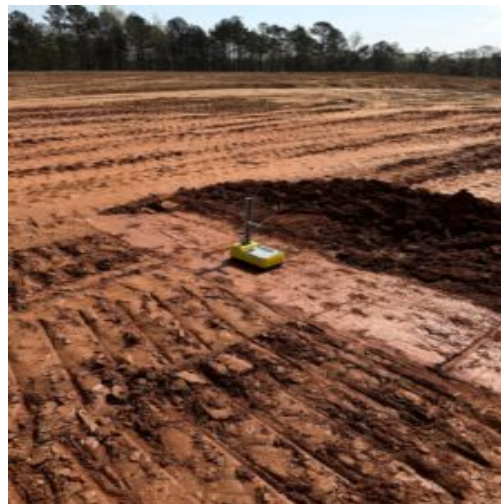

Date : 03/27/2026
Project No : 2025C149
Client Company : Davidson Homes
Arrival Time : 03/27/2026 08:00
Onsite Hours : 06:00

ASEC Report ID : 92034
Name of the Project : Grove at E. Thompson Mill Rd
Project Location : Buford
Weather : sunny
Departure Time : 03/27/2026 14:00
ASEC Technician Name : Samara Simha Reddy Kandi



Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
