

Date : 07/07/2025
Project No : 2025C160
Client Company : Artisan
Arrival Time : 07/07/2025 07:30
Onsite Hours : 05:30


ASEC Report ID : 82881
Name of the Project : Rockmart Township - 115 Felton Drive
Project Location : Rockmart
Weather : sunny
Departure Time : 07/07/2025 13:00
ASEC Technician Name :

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Our ASEC representative was on site as requested by the contractor (Wilbanks) for the observation/testing of the placement of fill/backfill. The technician observed the contractor spread one lift, approximately 8 to 12 inches in thickness, across the approximate location of Lots #65 through #75. The lift was compacted using a sheep-foot roller.

The technician performed a proctor point check in the roadway near SSMH2.0 for the previous workday tests. The technician provided the test results to the contractor. All roadway tests were found to meet job specifications for phase 1.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

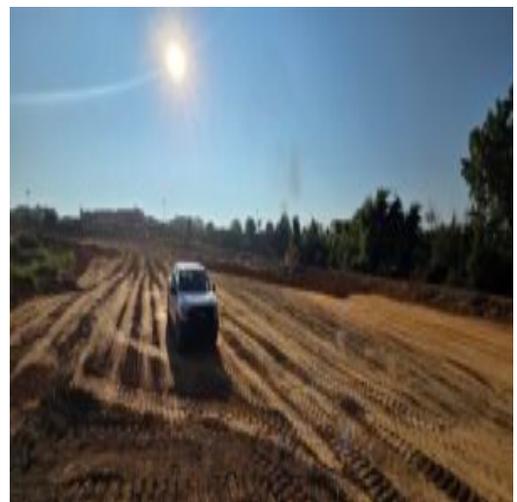

Date : 07/07/2025
Project No : 2025C160
Client Company : Artisan
Arrival Time : 07/07/2025 07:30
Onsite Hours : 05:30

ASEC Report ID : 82881
Name of the Project : Rockmart Township - 115 Felton Drive
Project Location : Rockmart
Weather : sunny
Departure Time : 07/07/2025 13:00
ASEC Technician Name :



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
