

Date : 07/24/2025
Project No : 2025C160
Client Company : Artisan
Arrival Time : 07/24/2025 08:45
Onsite Hours : 07:45

ASEC Report ID : 83308
Name of the Project : Rockmart Township - 115 Felton Drive
Project Location : Rockmart
Weather : sunny
Departure Time : 07/24/2025 16:30
ASEC Technician Name : Sean Willett


As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Our ASEC representative was on site to observe the contractor (Wilbanks) continue the placement of fill across the site.

The contractor placed lifts of approx. 8in to 12in in thickness across Lots #197 - 208 and #215 - #224. The technician performed density testing and provided test results to the contractor.

The contractor stripped topsoil from approximate areas of Lots #50 - #60 and requested our representative to observe a proof-roll of this area first thing in the morning.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

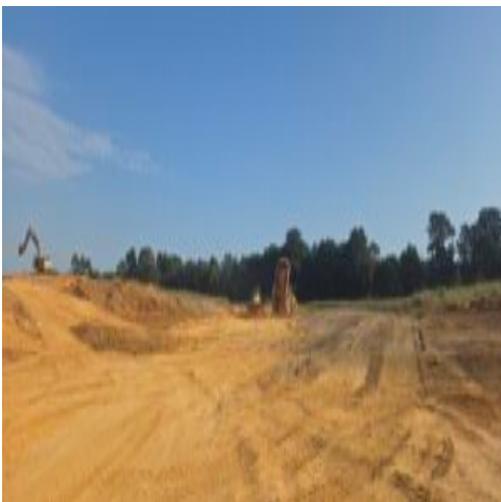

Date : 07/24/2025
Project No : 2025C160
Client Company : Artisan
Arrival Time : 07/24/2025 08:45
Onsite Hours : 07:45

ASEC Report ID : 83308
Name of the Project : Rockmart Township - 115 Felton Drive
Project Location : Rockmart
Weather : sunny
Departure Time : 07/24/2025 16:30
ASEC Technician Name : Sean Willett



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
