


Date : 10/07/2025
Project No : 2025C216
Client Company : Artisan
Arrival Time : 10/07/2025 14:00
Onsite Hours : 03:30

ASEC Report ID : 86598
Name of the Project : NW (Lots) Unit 4 PH 1A & 1B
Project Location : Dallas
Weather : cloudy
Departure Time : 10/07/2025 17:30
ASEC Technician Name : Clyde Smith

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

On the above date our representative to observe the grading contractor continue fill placement and compacting efforts for the building pads. The writer observed proof-rolling of completed building Lots #23, 24, 25, 26, 20, 19, 10 and 9. The proof-roll was observed using a loaded off-road rock dump truck making two passes over all areas. The subgrade soils appeared stable under traffic with no apparent movement. The proof-rolls appeared to verify subgrade stability suitable for the placement of fill. Density tests will be performed tomorrow with observation of the remaining completed lots. The writer also observed Advance Drilling contractor on site continuing drilling at east side road embankment.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

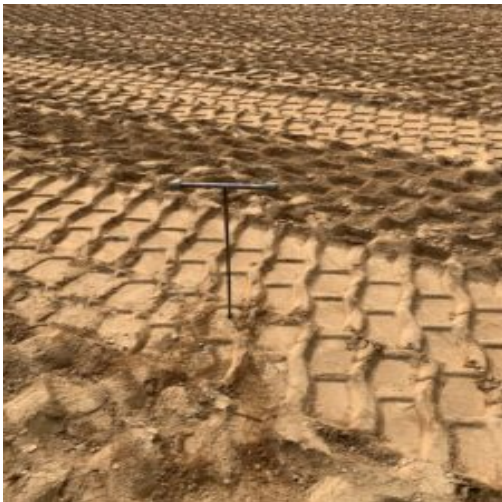


Proof rolling building lots sub grades




Date : 10/07/2025
Project No : 2025C216
Client Company : Artisan
Arrival Time : 10/07/2025 14:00
Onsite Hours : 03:30

ASEC Report ID : 86598
Name of the Project : NW (Lots) Unit 4 PH 1A & 1B
Project Location : Dallas
Weather : cloudy
Departure Time : 10/07/2025 17:30
ASEC Technician Name : Clyde Smith

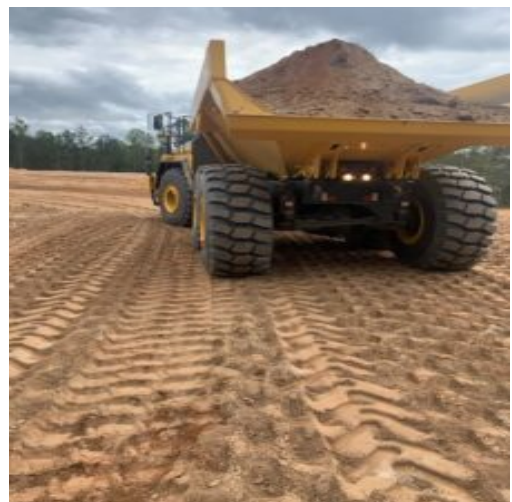

Date : 10/07/2025
Project No : 2025C216
Client Company : Artisan
Arrival Time : 10/07/2025 14:00
Onsite Hours : 03:30

ASEC Report ID : 86598
Name of the Project : NW (Lots) Unit 4 PH 1A & 1B
Project Location : Dallas
Weather : cloudy
Departure Time : 10/07/2025 17:30
ASEC Technician Name : Clyde Smith

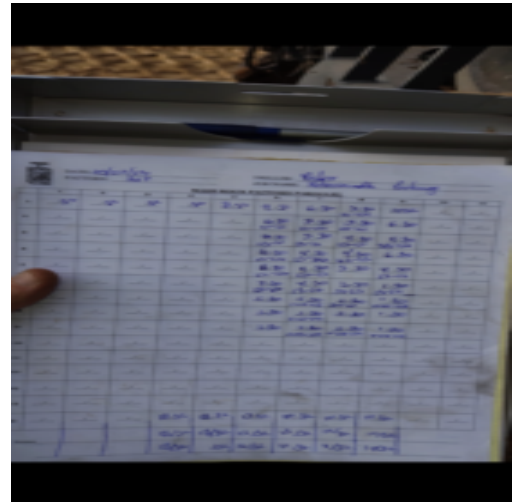

Drilling log 10/7/25

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
