

Date : 12/20/2025
Project No : 2021C060
Client Company : Pulte Group
Arrival Time : 12/20/2025 11:00
Onsite Hours : 01:30

ASEC Report ID : 88674
Name of the Project : Suncity - Peachtree
Project Location : Griffin, GA
Weather : Sunny
Departure Time : 12/20/2025 12:30
ASEC Technician Name : Sean Willett

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Our ASEC representative was on site as requested by the contractor (Pulte Homes) for mono-slab inspections and DCP testing of footings for lots #68 and #80 in pod #21.

Upon arrival to the site, it appeared that the footings have approx. 1in to 2in of water present. The contractor used plastic in the footings to protect them from rainfall. There was an approx. 10ft to 12ft stretch of the footing that was uncovered. ASEC performed DCP testing in these areas.

ASEC also probe rodded through the plastic in dry areas, and in-between the plastic and shoring in areas where water was present. Probe rod testing appeared to pass, and the slabs appear to be ready for pour once the water is removed/dried from the footings.


ASEC contacted Robert (Pulte) and informed him of the water standing in the footings. Once the water is removed, they are ready for pour.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



Date : 12/20/2025
 Project No : 2021C060
 Client Company : Pulte Group
 Arrival Time : 12/20/2025 11:00
 Onsite Hours : 01:30

ASEC Report ID : 88674
 Name of the Project : Suncity - Peachtree
 Project Location : Griffin, GA
 Weather : Sunny
 Departure Time : 12/20/2025 12:30
 ASEC Technician Name : Sean Willett

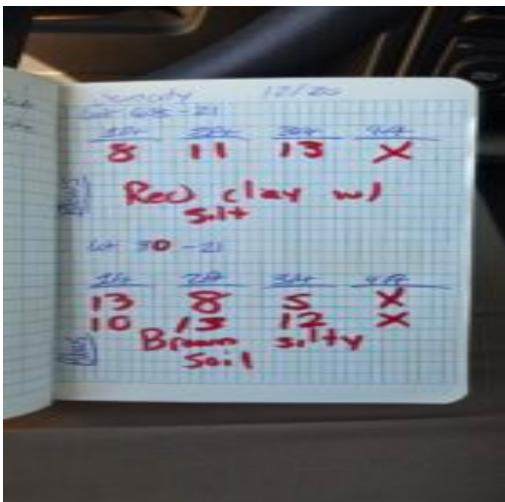

Date : 12/20/2025
Project No : 2021C060
Client Company : Pulte Group
Arrival Time : 12/20/2025 11:00
Onsite Hours : 01:30

ASEC Report ID : 88674
Name of the Project : Suncity - Peachtree
Project Location : Griffin, GA
Weather : Sunny
Departure Time : 12/20/2025 12:30
ASEC Technician Name : Sean Willett



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
