

Date : 06/17/2025
Project No : 2023C159
Client Company : CW Matthews
Arrival Time : 21:45
Onsite Hours : 10:15

ASEC Report ID : 82304
Name of the Project : Airfield Repairs 2021-23
Project Location : HJAlA, Atlanta, GA
Weather :
Departure Time : 08:00
ASEC Technician Name :

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.


The taxiway spalls were identified and marked. Cracked concrete was removed using various hand tools and machines.

After the concrete was broken and the space was prepared, concrete pouring began.

One set of four (4) beams were cast.

Previously cast beams were transported to the CWM lab.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

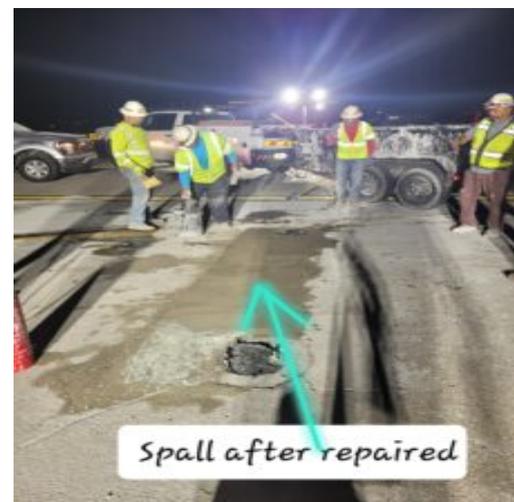

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
