

Date : 04/25/2026
Project No : 2023C159
Client Company : CW Matthews
Arrival Time : 04/25/2026
Onsite Hours : N/A

ASEC Report ID : 93715
Name of the Project : Airfield Repairs 2021-23
Project Location : HJAIA, Atlanta, GA
Weather : overcast
Departure Time : 04/26/2026
ASEC Technician Name : Russell Hendrix

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day:

Area 1

Excess soil was removed from the site. A concrete box (Type B inlet) was installed adjacent to an existing drainage structure. An approximately 26-inch core was drilled into the side of the existing structure to connect the two systems. M10 sand was placed and compacted using a trench packer. Compaction testing was performed with a Troxler 3430 (refer to testing report). Topsoil was then delivered and placed using a cultipacking attachment.

Area 3

Upon arrival, the final lift had been placed and was undergoing compaction with a ride-on vibratory sheepsfoot roller. Compaction testing was performed using a Troxler 3430 (see testing report). Following successful completion of the final lift and testing, topsoil was delivered to the area.

Area 4


On the west side of Area 4, backfill for the second lift above the drain pipe was tested after compaction and determined to have excessively high moisture content (see testing report). The material was removed and replaced; however, the replacement soil also exhibited unacceptable moisture levels. Upon recommendation from 2MNext, graded aggregate base (GAB) was mixed with the existing soil to reduce overall moisture content. Refer to the testing report for results. Excess soil was hauled offsite.

Area 6

Graded aggregate base (GAB) was placed.

Date : 04/25/2026
Project No : 2023C159
Client Company : CW Matthews
Arrival Time : 04/25/2026
Onsite Hours : N/A


ASEC Report ID : 93715
Name of the Project : Airfield Repairs 2021-23
Project Location : HJAIA, Atlanta, GA
Weather : overcast
Departure Time : 04/26/2026
ASEC Technician Name : Russell Hendrix

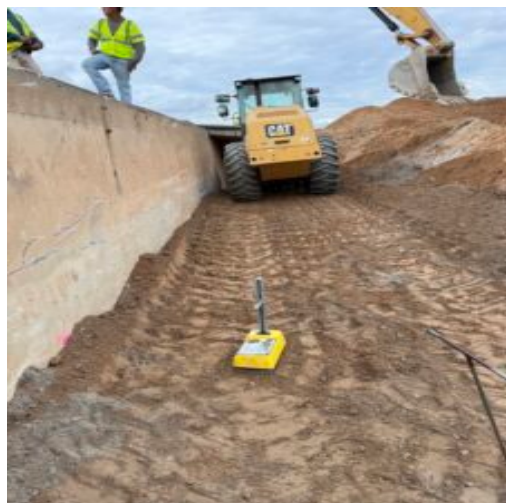

Testing Area 4



Backfilling Area 4

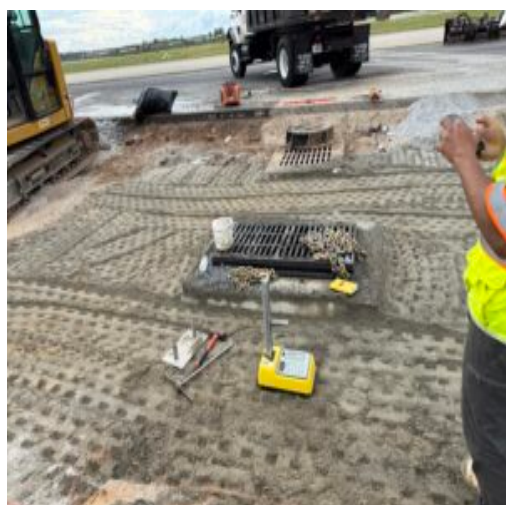

Testing area 1



Area 1

Date : 04/25/2026
Project No : 2023C159
Client Company : CW Matthews
Arrival Time : 04/25/2026
Onsite Hours : N/A


ASEC Report ID : 93715
Name of the Project : Airfield Repairs 2021-23
Project Location : HJAI, Atlanta, GA
Weather : overcast
Departure Time : 04/26/2026
ASEC Technician Name : Russell Hendrix



Area 1



Area 4

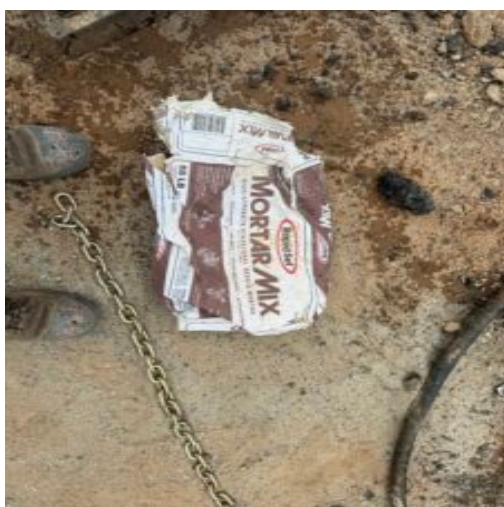

Mix used to for collar area 1 drain



Area 1

Date : 04/25/2026
Project No : 2023C159
Client Company : CW Matthews
Arrival Time : 04/25/2026
Onsite Hours : N/A

ASEC Report ID : 93715
Name of the Project : Airfield Repairs 2021-23
Project Location : HJAI, Atlanta, GA
Weather : overcast
Departure Time : 04/26/2026
ASEC Technician Name : Russell Hendrix




Area 1 box placement



Compacting



Area 1

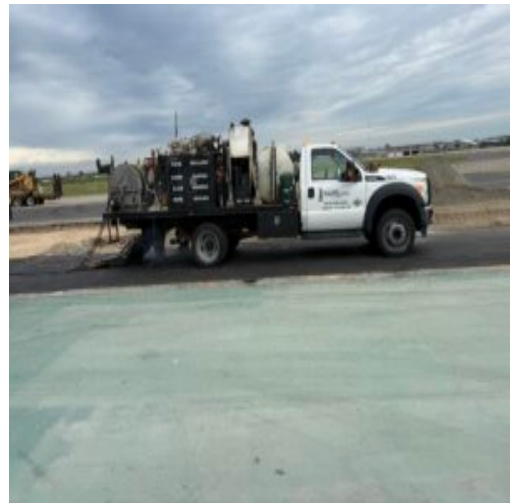

ABC Coring for location 1 drain box

Date : 04/25/2026
Project No : 2023C159
Client Company : CW Matthews
Arrival Time : 04/25/2026
Onsite Hours : N/A

ASEC Report ID : 93715
Name of the Project : Airfield Repairs 2021-23
Project Location : HJAIA, Atlanta, GA
Weather : overcast
Departure Time : 04/26/2026
ASEC Technician Name : Russell Hendrix



Pipe used between boxes area 1



Hauling out extra material



compacting



compacted area

Date : 04/25/2026
Project No : 2023C159
Client Company : CW Matthews
Arrival Time : 04/25/2026
Onsite Hours : N/A

ASEC Report ID : 93715
Name of the Project : Airfield Repairs 2021-23
Project Location : HJAIA, Atlanta, GA
Weather : overcast
Departure Time : 04/26/2026
ASEC Technician Name : Russell Hendrix



Cultipacking



Cultipacking



Soil removal



spreading topsoil

Date : 04/25/2026
Project No : 2023C159
Client Company : CW Matthews
Arrival Time : 04/25/2026
Onsite Hours : N/A

ASEC Report ID : 93715
Name of the Project : Airfield Repairs 2021-23
Project Location : HJAIA, Atlanta, GA
Weather : overcast
Departure Time : 04/26/2026
ASEC Technician Name : Russell Hendrix



Testing



Hauling out soil



Compacting



Compacted area

Date : 04/25/2026
Project No : 2023C159
Client Company : CW Matthews
Arrival Time : 04/25/2026
Onsite Hours : N/A

ASEC Report ID : 93715
Name of the Project : Airfield Repairs 2021-23
Project Location : HJAI, Atlanta, GA
Weather : overcast
Departure Time : 04/26/2026
ASEC Technician Name : Russell Hendrix



Testing



Preparing

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
