

Date : 08/08/2025
Project No : 2023C180
Client Company : Artisan Communities
Arrival Time : 08/08/2025 8:30
Onsite Hours : 06:30

ASEC Report ID : 84454
Name of the Project : Lakeside Sub., Lovers Lane > Retaining
Wall
Project Location : Calhoun
Weather : sunny
Departure Time : 08/08/2025 15:00
ASEC Technician Name : Aminullah Azimi

At the request of the client's representative, our AS ENGINEERING AND CONSULTING, LLC (ASEC) representative visited the job site to observe the contractor's work activities from a quality standpoint to verify compliance with project drawings/specifications, applicable codes, and materials submittals and conducted QC testing per the project drawings and specifications. The following observations were made during our evaluation:

Our ASEC representative to observe the placement of MSE retaining walls. It was noted that the base course was backfilled behind the blocks and the cells with No. 57 stone. Every 2nd course a geotextile fabric was placed followed by an 8-inch compacted lift. No. 57 stone was utilized 1-foot behind the block and within the cells. No remedial recommendation was required.

NOTE: On this day, Density testing was performed which failed due to high in-situ moisture contents being higher than the optimum moisture limit. It was recommended to scarify and aerate these soils following by recompaction.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.





Date : 08/08/2025
Project No : 2023C180
Client Company : Artisan Communities
Arrival Time : 08/08/2025 8:30
Onsite Hours : 06:30

ASEC Report ID : 84454
Name of the Project : Lakeside Sub., Lovers Lane > Retaining
Wall
Project Location : Calhoun
Weather : sunny
Departure Time : 08/08/2025 15:00
ASEC Technician Name : Aminullah Azimi



Date : 08/08/2025
Project No : 2023C180
Client Company : Artisan Communities
Arrival Time : 08/08/2025 8:30
Onsite Hours : 06:30

ASEC Report ID : 84454
Name of the Project : Lakeside Sub., Lovers Lane > Retaining
Wall
Project Location : Calhoun
Weather : sunny
Departure Time : 08/08/2025 15:00
ASEC Technician Name : Aminullah Azimi

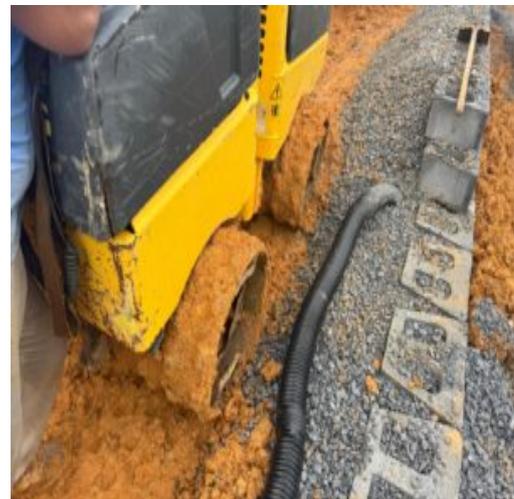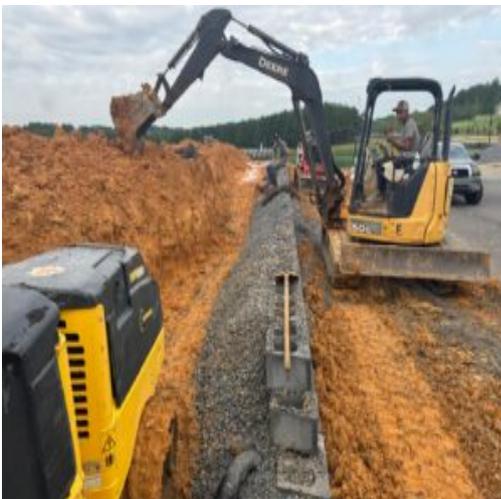

Date : 08/08/2025
Project No : 2023C180
Client Company : Artisan Communities
Arrival Time : 08/08/2025 8:30
Onsite Hours : 06:30

ASEC Report ID : 84454
Name of the Project : Lakeside Sub., Lovers Lane > Retaining
Wall
Project Location : Calhoun
Weather : sunny
Departure Time : 08/08/2025 15:00
ASEC Technician Name : Aminullah Azimi



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
