

Date : 09/06/2024
Project No : 2024C116
Client Company : Peeples Owner, LLC
Arrival Time : 09/06/2024 08:30
Onsite Hours : 9:00

ASEC Report ID : 69544
Name of the Project : Peeples Valley Rd, Overlook at Pettit
Project Location : Cartersville
Weather : Cloudy
Departure Time : 09/06/2024 17:30
ASEC Technician Name : Fawad Shagiwal

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawings/specifications, applicable codes and material submittals.

The following observations were observed on the site this day.

- Continuation of the placement and compaction of backfill soil for Lots #89 to #97 was progressed with 1-foot lifts being placed and compacted using a sheeps-foot compactor (CP54B), (RA30), (D61PX) and (CAT330).
- Excavation and placement of storm water lines and manholes progressed.
- Installation and placement of sewer lines and manhole SSA4 progressed.
- Installation and placement of storm water lines from manhole CIA11 to CIA12 progressed.
- Installation and placement of storm water manholes CIA11 and CIA12 progressed.
- One (1) foot lifts were being placed and compacted at the trench between storm water manholes CIA11 and CIA12 using trench packer (BMP8500) and sheeps-foot (CP54B) equipment.
- Two (2) foot lifts were placed and compacted for the trench to sewer manhole SSA4.
- Density test results indicate that the compacted material met the project requirements of 95% the maximum dry density obtained by the (Standard Proctor ASTM 698).




Date : 09/06/2024
Project No : 2024C116
Client Company : Peeples Owner, LLC
Arrival Time : 09/06/2024 08:30
Onsite Hours : 9:00

ASEC Report ID : 69544
Name of the Project : Peeples Valley Rd, Overlook at Pettit
Project Location : Cartersville
Weather : Cloudy
Departure Time : 09/06/2024 17:30
ASEC Technician Name : Fawad Shagiwal



Date : 09/06/2024
Project No : 2024C116
Client Company : Peeples Owner, LLC
Arrival Time : 09/06/2024 08:30
Onsite Hours : 9:00

ASEC Report ID : 69544
Name of the Project : Peeples Valley Rd, Overlook at Pettit
Project Location : Cartersville
Weather : Cloudy
Departure Time : 09/06/2024 17:30
ASEC Technician Name : Fawad Shagiwal

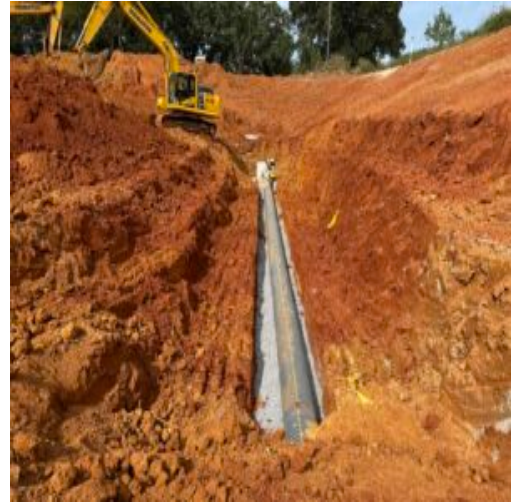

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
