

Date : 02/24/2025
 Project No : 2024C168
 Client Company : Century Communities
 Arrival Time : 02/24/2025 9:00
 Onsite Hours : 06:00


ASEC Report ID : 77994
 Name of the Project : Reserve @ Gum Springs
 Project Location : Jefferson, Jackson County, Georgia
 Weather : sunny
 Departure Time : 02/24/2025 15:00
 ASEC Technician Name : Aminullah Azimi

Our AS Engineering & Consulting (ASEC) representative arrived on site to observe field activities. The following tasks were performed:

Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

- The placement and compaction of backfill soils for the sewer trench between MHSA3 and MHSM1 continued this day.
- At the time of arrival, our representative observed that work was in progress with 1-foot lifts being placed and compacted using 14-ton sheeps-foot and trench compaction equipment. Compaction testing was performed using the Standard Test Method for Density of Soil in Place by Drive-Cylinder (ASTM D 2937), along with general probing using a 3/8" diameter probe rod.
- Density test results indicate that most of the compacted materials met the project requirement of 95% of the maximum dry density obtained by a Standard Proctor ASTM 698.
- Note: Moisture contents were found to be outside specified moisture content range.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

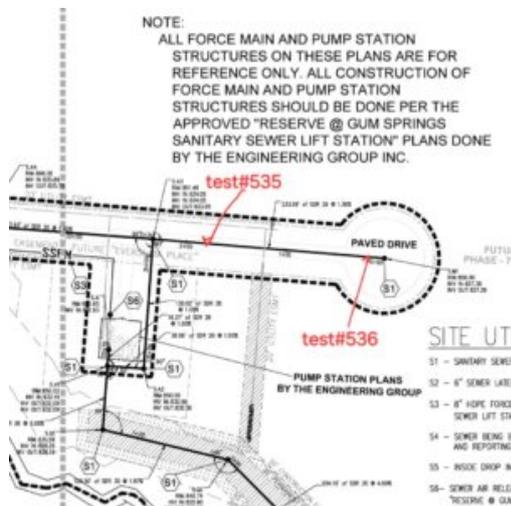

Date : 02/24/2025
Project No : 2024C168
Client Company : Century Communities
Arrival Time : 02/24/2025 9:00
Onsite Hours : 06:00

ASEC Report ID : 77994
Name of the Project : Reserve @ Gum Springs
Project Location : Jefferson, Jackson County, Georgia
Weather : sunny
Departure Time : 02/24/2025 15:00
ASEC Technician Name : Aminullah Azimi



Date : 02/24/2025
Project No : 2024C168
Client Company : Century Communities
Arrival Time : 02/24/2025 9:00
Onsite Hours : 06:00

ASEC Report ID : 77994
Name of the Project : Reserve @ Gum Springs
Project Location : Jefferson, Jackson County, Georgia
Weather : sunny
Departure Time : 02/24/2025 15:00
ASEC Technician Name : Aminullah Azimi



Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
