

Date : 02/17/2025  
Project No : 2024C202  
Client Company : CCG  
Arrival Time : 02/17/2025 08:30  
Onsite Hours : 01:15

ASEC Report ID : 77407  
Name of the Project : Old Griffin Rd - Hawthorne Reserve  
Project Location : Dallas  
Weather : Clear sky  
Departure Time : 02/17/2025 09:45  
ASEC Technician Name : Solomon Cherie

---


Our AS Engineering & Consulting (ASEC) representative arrived on site to observe field activities. The following tasks were performed:

The project site is still very wet and muddy. After consultation with the grading contractor, it was decided to postpone cutting and filling activities to concentrate on site dewatering and demucking.

Please contact us if you have any questions regarding this report.




Picture showing water ponds still not dry

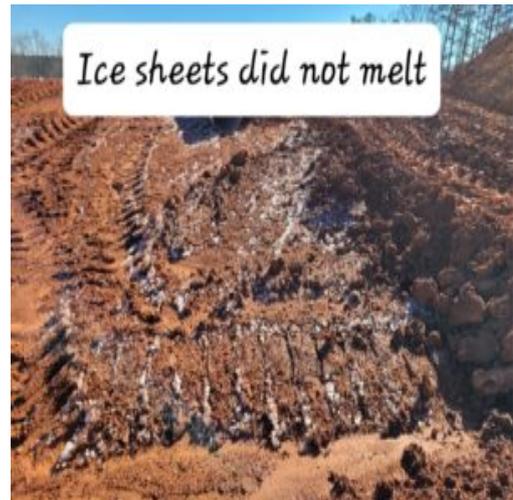

Picture depicting ice sheets not yet melted

Date : 02/17/2025  
Project No : 2024C202  
Client Company : CCG  
Arrival Time : 02/17/2025 08:30  
Onsite Hours : 01:15

ASEC Report ID : 77407  
Name of the Project : Old Griffin Rd - Hawthorne Reserve  
Project Location : Dallas  
Weather : Clear sky  
Departure Time : 02/17/2025 09:45  
ASEC Technician Name : Solomon Cherie

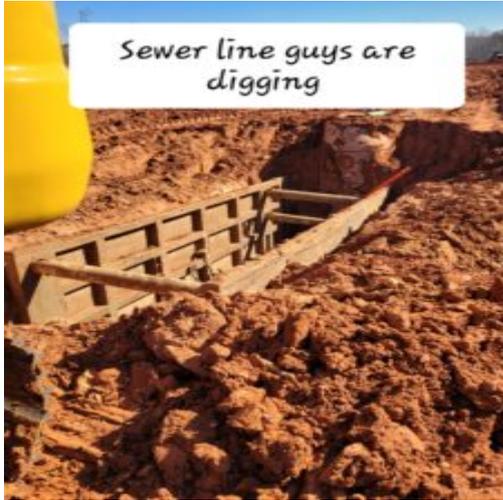

Sewer line b/n Manholes A14 and A14.5

*Kenneth Mosman*

**Kenneth Mosman**

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
