

Date : 02/21/2025
Project No : 2024C202
Client Company : CCG
Arrival Time : 02/21/2025 07:45
Onsite Hours : 07:45


ASEC Report ID : 77749
Name of the Project : Old Griffin Rd - Hawthorne Reserve
Project Location : Dallas
Weather : Sunny
Departure Time : 02/21/2025 15:30
ASEC Technician Name : Solomon Cherie

Our AS Engineering & Consulting (ASEC) representative arrived on site to observe field activities. The following tasks were performed:

Observed cutting and fill placemen activities as performed by a 349E CAT excavator and hauled using 745C tandem-axled dump trucks. Soils were spread by a 61Pxi Komatsu Bulldozer and compaction using an 815F CAT Roller.

Compaction did not meet job specifications. The contractor was informed, and the area was recompactd with some improvement in compaction testing. However, this area still requires additional effort to meet job specifications.

Please contact us if you have any questions regarding this report or of the density test results.

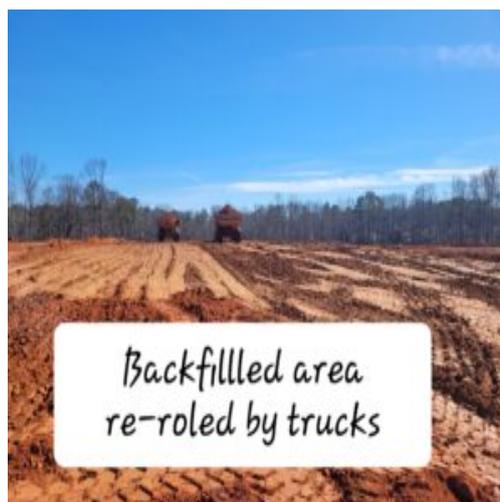

Backfilled, rolled and re-rolled to improve compaction.

Kenneth Mosman

Kenneth Mosman

Date : 02/21/2025
Project No : 2024C202
Client Company : CCG
Arrival Time : 02/21/2025 07:45
Onsite Hours : 07:45

ASEC Report ID : 77749
Name of the Project : Old Griffin Rd - Hawthorne Reserve
Project Location : Dallas
Weather : Sunny
Departure Time : 02/21/2025 15:30
ASEC Technician Name : Solomon Cherie

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
