

Date : 02/25/2025
Project No : 2024C202
Client Company : CCG
Arrival Time : 02/25/2025 07:45
Onsite Hours : 06:00


ASEC Report ID : 78066
Name of the Project : Old Griffin Rd - Hawthorne Reserve
Project Location : Dallas
Weather : Sunny
Departure Time : 02/25/2025 13:45
ASEC Technician Name : Solomon Cherie

Our AS Engineering & Consulting (ASEC) representative arrived on site to observe field activities. The following tasks were performed:

Observed the placement of fill/grading for Lots #26 through #31 today. The results displayed very high moisture contents (resulting in low compaction). The superintendent was informed to scarify and aerate surficial wet soils then recompact. Results are attached in separate reports.

Sewer lines between Manholes E3 & E4 and A14 & A15 were backfilled and compacted today.

Please contact us if you have any questions regarding this report or of the density test results.

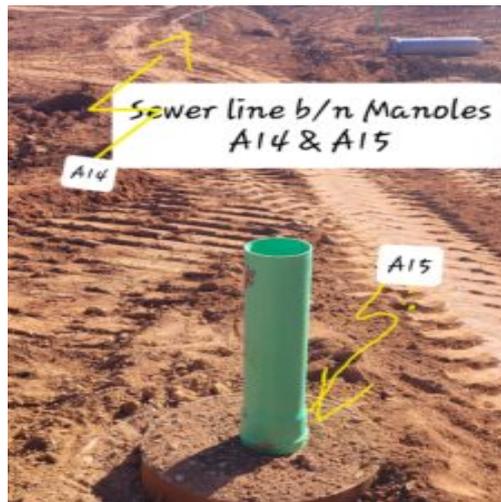

Sewer line backfilled and packed

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
