


Date : 03/26/2025
Project No : 2024C202
Client Company : CCG
Arrival Time : 03/26/2025 08:00
Onsite Hours : 04:30

ASEC Report ID : 79097
Name of the Project : Old Griffin Rd - Hawthorne Reserve
Project Location : Dallas
Weather : Clear sky
Departure Time : 03/26/2025 12:30
ASEC Technician Name : Solomon Cherie

Our AS Engineering & Consulting (ASEC) representative arrived on site to observe field activities. The following tasks were performed:

Observed the placement of fill/grading for Lots #62 and #63 today. Compaction tests were performed using a nuclear density gauge. Overall, the results of density testing did not meet the project and ASTM requirements due to excessive moisture contents. Contractor was recommended to scarify and aerate prior to recompaction. Results are attached in separate reports.

Please contact us if you have any questions regarding this report or of the density test results.

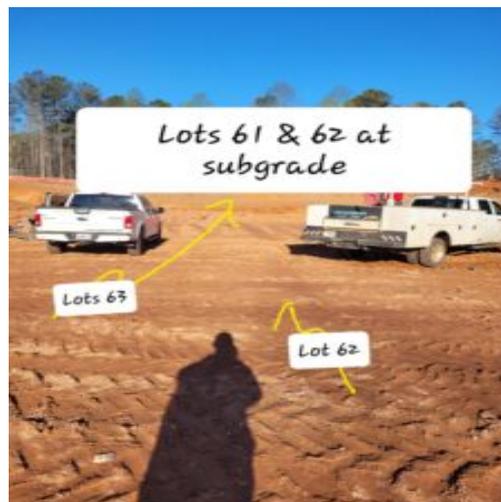

Picture depicting Lots 62 & 63 at subgrade

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
