


Date : 04/17/2025
Project No : 2024C213
Client Company : WDG
Arrival Time : 04/17/2025 8:00
Onsite Hours : 9:30

ASEC Report ID : 81157
Name of the Project : Covington Town Center PH II
Project Location : Covington, GA
Weather : sunny
Departure Time : 04/17/2025 17:30
ASEC Technician Name : Aminullah Azimi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.


- The placement and compaction of fill for the storm trench from MHA0, MHB1, MHB2 and MHB3, sewer trench between existing MH to front of building, continued this day.
- At the time of arrival, our representative observed that work was in progress with 1-foot lifts being placed and compacted using a 9-ton sheeps-foot and trench compactors. Compaction testing was performed using a Troxler nuclear density gauge of Soil (ASTM D 2937), along with general probing using a 3/8" diameter probe rod.
- Density test results indicate that most of the compacted materials met the project requirement of 95% of the maximum dry density obtained by a Standard Proctor ASTM 698.
- Note: contractor used soils with various diameter of rock embedded (see attached photos).

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

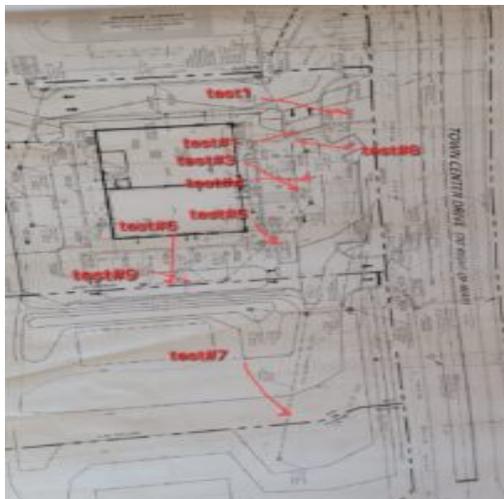

Date : 04/17/2025
Project No : 2024C213
Client Company : WDG
Arrival Time : 04/17/2025 8:00
Onsite Hours : 9:30

ASEC Report ID : 81157
Name of the Project : Covington Town Center PH II
Project Location : Covington, GA
Weather : sunny
Departure Time : 04/17/2025 17:30
ASEC Technician Name : Aminullah Azimi

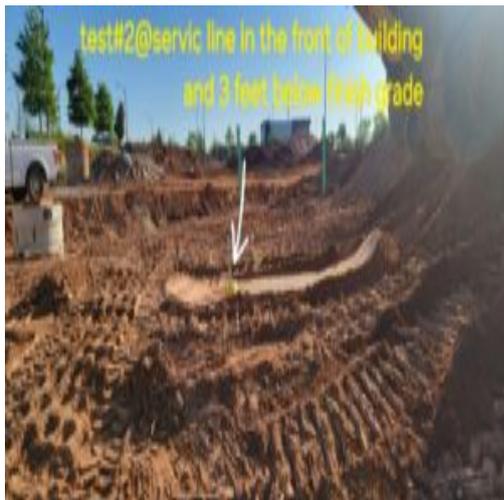

Date : 04/17/2025
Project No : 2024C213
Client Company : WDG
Arrival Time : 04/17/2025 8:00
Onsite Hours : 9:30

ASEC Report ID : 81157
Name of the Project : Covington Town Center PH II
Project Location : Covington, GA
Weather : sunny
Departure Time : 04/17/2025 17:30
ASEC Technician Name : Aminullah Azimi



Date : 04/17/2025
Project No : 2024C213
Client Company : WDG
Arrival Time : 04/17/2025 8:00
Onsite Hours : 9:30

ASEC Report ID : 81157
Name of the Project : Covington Town Center PH II
Project Location : Covington, GA
Weather : sunny
Departure Time : 04/17/2025 17:30
ASEC Technician Name : Aminullah Azimi



Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
