

Date : 06/24/2025
Project No : 2024C213
Client Company : WDG
Arrival Time : 06/24/2025 12:30
Onsite Hours : 01:00

ASEC Report ID : 82533
Name of the Project : Covington Town Center PH II
Project Location : Covington, GA
Weather : sunny
Departure Time : 06/24/2025 13:30
ASEC Technician Name : Sean Willett

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

On the above date, the technician was onsite as requested by the contractor (Fulcrum) for the observation/testing of soils.


The contractor (Buck) showed the technician an electrical conduit trench on the south and southeast side of main building. The trench appeared to be approximately 1 to 2 feet in depth. The contractor had begun placing fill in the trench and requested the technician to visually inspect and to verify stability if possible. The fill mostly consisted of very large pieces of blasted rock. The technician was unable to conduct any density testing due to large, rocky materials being used to backfill this trench. The technician recommended that the contractor remove the blasted rock and backfill with either No. 57 stone or suitable fill. There is a possibility that the blasted rock fragments will damage the conduit if the contractor attempts to compact this area with heavy compaction equipment. The contractor agreed will retain a copy of our report (included with photos) for their records.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



Date : 06/24/2025
Project No : 2024C213
Client Company : WDG
Arrival Time : 06/24/2025 12:30
Onsite Hours : 01:00

ASEC Report ID : 82533
Name of the Project : Covington Town Center PH II
Project Location : Covington, GA
Weather : sunny
Departure Time : 06/24/2025 13:30
ASEC Technician Name : Sean Willett

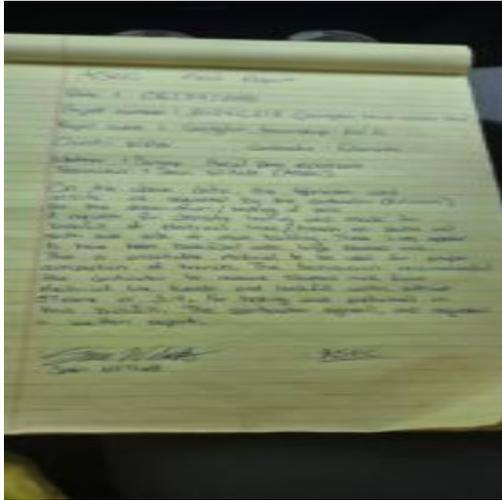

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
