


Date : 10/04/2024
Project No : 2024C217
Client Company : Artisan
Arrival Time : 10/04/2024 08:15
Onsite Hours : 08:30

ASEC Report ID : 71530
Name of the Project : Naturewalk - 7 Hills Amenities
Project Location : Dallas
Weather : sunny
Departure Time : 10/04/2024 16:45
ASEC Technician Name : Vamsi Polisetty

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

- Upon arrival, the contractor was engaged in excavations using a Komatsu PC 360LC on the west of the project site. They were also doing cut with a Komatsu PC210LC. Fill was being transported with two tandem dump trucks, while dozing was performed with a Komatsu 39PX and a D85EX. Compaction work was carried out using a CAT 563 E. Backfilling with boulders fill under the tennis court with proof-rolling performed following placement.
- Compaction testing was performed using a Troxler nuclear density gauge, along with general probing using a 3/8" diameter probe rod on the club House area.
- Density test results indicate that compacted materials did meet the project requirement of 95% of the maximum dry density obtained by a Standard Proctor ASTM 698.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you

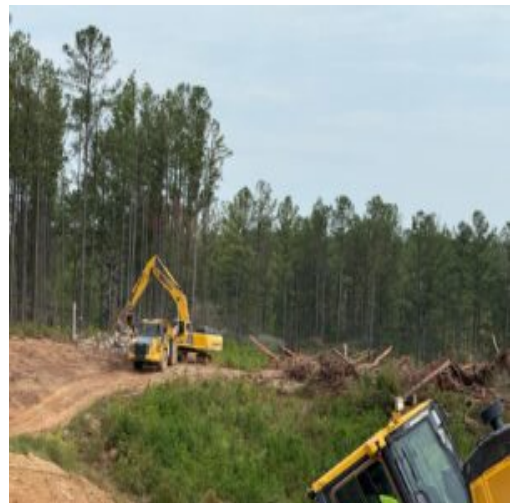

Date : 10/04/2024
Project No : 2024C217
Client Company : Artisan
Arrival Time : 10/04/2024 08:15
Onsite Hours : 08:30

ASEC Report ID : 71530
Name of the Project : Naturewalk - 7 Hills Amenities
Project Location : Dallas
Weather : sunny
Departure Time : 10/04/2024 16:45
ASEC Technician Name : Vamsi Polisetty



Date : 10/04/2024
Project No : 2024C217
Client Company : Artisan
Arrival Time : 10/04/2024 08:15
Onsite Hours : 08:30

ASEC Report ID : 71530
Name of the Project : Naturewalk - 7 Hills Amenities
Project Location : Dallas
Weather : sunny
Departure Time : 10/04/2024 16:45
ASEC Technician Name : Vamsi Polisetty



Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
