

Date : 11/11/2024
Project No : 2024C217
Client Company : Artisan
Arrival Time : 11/11/2024 07:35
Onsite Hours : 9:30

ASEC Report ID : 73434
Name of the Project : Naturewalk - 7 Hills Amenities
Project Location : Dallas
Weather : cloudy/rainy
Departure Time : 11/11/2024 17:00
ASEC Technician Name : Vamsi Polisetty

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Seven Hills: Amenities


- Large boulders were encountered during grading and the breaking of rock boulders was done using a Deere 350GL.
- Upon arrival, the contractor was engaged in cutting the roadway using a Komatsu PC 360LC and cut from the west of the job site. Fill was being transported with two tandem dumps for the tennis Court and parking lot, while dozing was performed with a Komatsu D85EX for the next layer and compacted using a CAT563E.
- The next lift of fill was started on the tennis court & parking area.
- Boulder fill placed was testing using proof-rolling to verify stability in lieu of density testing.
- Compaction testing was performed using a Troxler nuclear density gauge, along with general probing using a 3/8" diameter probe rod for fill placed on the clubhouse area.
- Density test results indicate that compacted materials did meet the project requirement of 95% of the maximum dry density obtained by a Standard Proctor ASTM 698.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you



Date : 11/11/2024
Project No : 2024C217
Client Company : Artisan
Arrival Time : 11/11/2024 07:35
Onsite Hours : 9:30

ASEC Report ID : 73434
Name of the Project : Naturewalk - 7 Hills Amenities
Project Location : Dallas
Weather : cloudy/rainy
Departure Time : 11/11/2024 17:00
ASEC Technician Name : Vamsi Polisetty

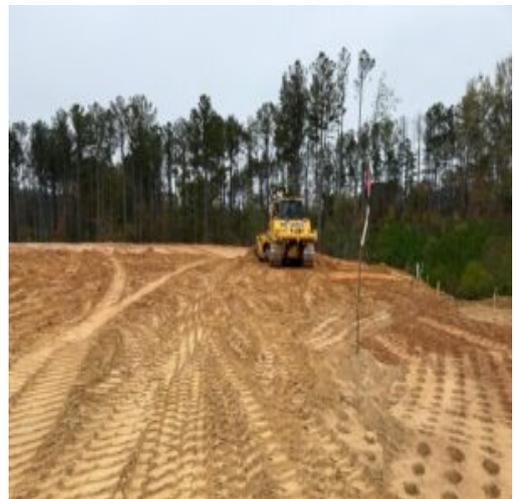

Date : 11/11/2024
Project No : 2024C217
Client Company : Artisan
Arrival Time : 11/11/2024 07:35
Onsite Hours : 9:30

ASEC Report ID : 73434
Name of the Project : Naturewalk - 7 Hills Amenities
Project Location : Dallas
Weather : cloudy/rainy
Departure Time : 11/11/2024 17:00
ASEC Technician Name : Vamsi Polisetty



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
