


Date : 07/10/2025
Project No : 2024C217
Client Company : Artisan
Arrival Time : 07/10/2025 8:30
Onsite Hours : 06:30

ASEC Report ID : 83411
Name of the Project : Naturewalk - 7 Hills Amenities
Project Location : Dallas
Weather : sunny
Departure Time : 07/10/2025 15:00
ASEC Technician Name : Aminullah Azimi

As requested, a representative from AS Engineering and Consulting (ASEC) visited the site to perform quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawings/specifications, applicable codes, and approved material submittals. The following observations were made during the site visit:


The contractor prepared the slope area located to the east of Lot #92 by removing all grass, organic material, and roots for a stable surface for soil placement. Some areas were too high for the dozer, so those areas were cleaned by labor using shovels. Following this, imported soil from an external source was delivered to the site and spread evenly across the prepared area and compacted using a dozer. In addition to the earthwork, the contractor cleaned the space between the water storage manholes using a hose to remove any accumulated debris.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

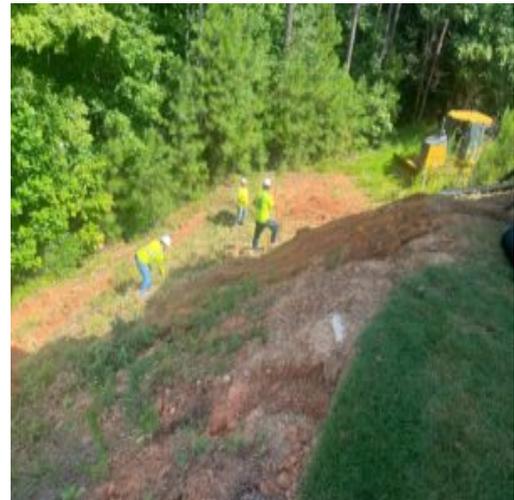

Date : 07/10/2025
Project No : 2024C217
Client Company : Artisan
Arrival Time : 07/10/2025 8:30
Onsite Hours : 06:30

ASEC Report ID : 83411
Name of the Project : Naturewalk - 7 Hills Amenities
Project Location : Dallas
Weather : sunny
Departure Time : 07/10/2025 15:00
ASEC Technician Name : Aminullah Azimi

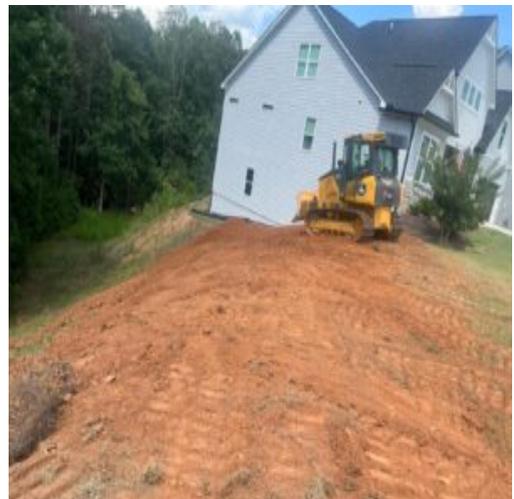

Date : 07/10/2025
Project No : 2024C217
Client Company : Artisan
Arrival Time : 07/10/2025 8:30
Onsite Hours : 06:30

ASEC Report ID : 83411
Name of the Project : Naturewalk - 7 Hills Amenities
Project Location : Dallas
Weather : sunny
Departure Time : 07/10/2025 15:00
ASEC Technician Name : Aminullah Azimi



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
