


Date : 09/12/2025
Project No : 2024C217
Client Company : Artisan
Arrival Time : 09/12/2025 10:00
Onsite Hours : 02:30

ASEC Report ID : 85906
Name of the Project : Naturewalk - 7 Hills Amenities
Project Location : Dallas
Weather : sunny
Departure Time : 09/12/2025 12:30
ASEC Technician Name : Sean Willett

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Our ASEC representative was on site for the observation/testing of the placement of GAB. Our ASEC representative met with the contractor and Mr. Keener of Paulding County DOT to perform a proof-roll of the previous placed GAB. The proof-roll still showed some pumping and rutting. It was agreed to undercut approximately 6 in of GAB in these areas and to replace with a thicker layer of asphalt. The contractor began to remove asphalt from a new cut in the road, but due to equipment breakdowns, they will not start excavation until next week.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

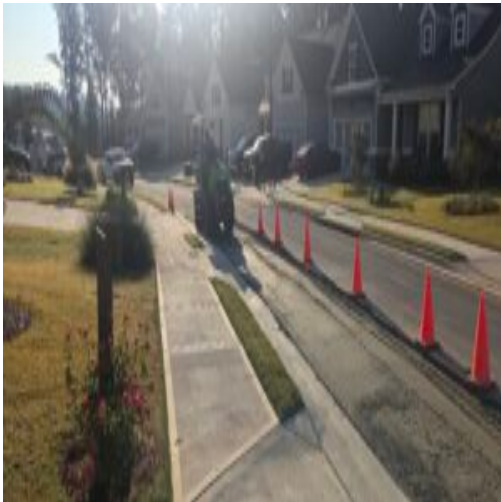

Date : 09/12/2025
Project No : 2024C217
Client Company : Artisan
Arrival Time : 09/12/2025 10:00
Onsite Hours : 02:30

ASEC Report ID : 85906
Name of the Project : Naturewalk - 7 Hills Amenities
Project Location : Dallas
Weather : sunny
Departure Time : 09/12/2025 12:30
ASEC Technician Name : Sean Willett



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
