



Daily Field Report


Date : 04/11/2026
Project No : 2024C217
Client Company : Artisan
Arrival Time : 04/11/2026 07:30
Onsite Hours : 03:00

ASEC Report ID : 92815
Name of the Project : Naturewalk - 7 Hills Amenities
Project Location : Dallas
Weather : Sunny
Departure Time : 04/11/2026 10:30
ASEC Technician Name : Clyde Smith


As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Our representative was on site and met with the county official Mr. Mike Jones to observe reinforcing steel at the pork chop at the amenities drive entrance on Seven Hills Boulevard. Several deficiencies were noted for repair with the rebar. The form work for curbing was not complete at the time of observation. The contractor was made aware of needed repairs which will be re-evaluated on 4/13/26.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

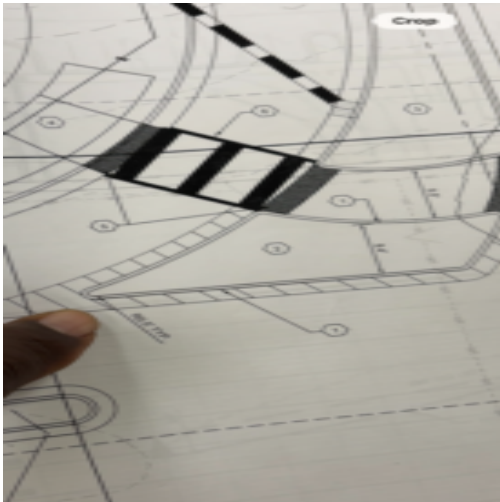

Reinforcing steel observed with deficiencies noted, radius not installed, mat steel not supported by dowels, and forming for curbing not completed.

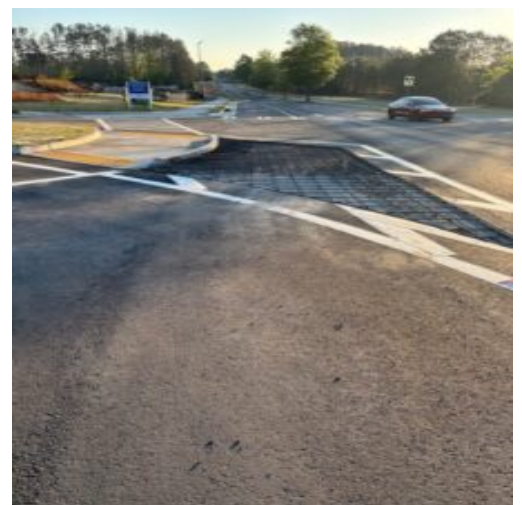



Daily Field Report

Date : 04/11/2026
Project No : 2024C217
Client Company : Artisan
Arrival Time : 04/11/2026 07:30
Onsite Hours : 03:00

ASEC Report ID : 92815
Name of the Project : Naturewalk - 7 Hills Amenities
Project Location : Dallas
Weather : Sunny
Departure Time : 04/11/2026 10:30
ASEC Technician Name : Clyde Smith



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
