

Date : 02/10/2025
Project No : 2024C315
Client Company : J. Chapman Const.
Arrival Time : 02/10/2025 09:00
Onsite Hours : 08:00

ASEC Report ID : 77425
Name of the Project : Cottages at Villa Rica - Rock Blasting
Project Location : Villa Rica
Weather : Cloudy
Departure Time : 02/10/2025 17:00
ASEC Technician Name : Micah Aycock

The aforementioned AS Engineering and Consulting (ASEC) representative visited the Cottages at Villa Rica site to monitor drilling and rock removal operations. The contractor performing the work was Precision Blasting. The following observations were made on-site:

Blasting Data:

The area blasted today was between lot #192 and lot #54 and for the lateral to lot 54. The center of the blast was a trench pattern and had mass rock patterns on either side. A total trench area blasted was 744 square feet. The calculated volume of trench rock blasted was 374.76 cubic yards. A total mass rock area blasted was 2,304 square feet with a with a calculated volume of 740.00 cubic yards rock blasted. These blasts created holes in the ground that were over 20 ft deep, the excavation team leveled the area after the blast to make it safer to walk around.

Drilling Data:

The drilling continued in the same pattern as before. Trench in the middle with mass rock patterns surrounding both sides. The team continued south towards lot #190 and lot #56.

We appreciate the opportunity to assist you with this project. Should you have any questions regarding this report, please do not hesitate to contact us. We would be happy to discuss it with you.





Date : 02/10/2025
Project No : 2024C315
Client Company : J. Chapman Const.
Arrival Time : 02/10/2025 09:00
Onsite Hours : 08:00

ASEC Report ID : 77425
Name of the Project : Cottages at Villa Rica - Rock Blasting
Project Location : Villa Rica
Weather : Cloudy
Departure Time : 02/10/2025 17:00
ASEC Technician Name : Micah Aycock



Date : 02/10/2025
 Project No : 2024C315
 Client Company : J. Chapman Const.
 Arrival Time : 02/10/2025 09:00
 Onsite Hours : 08:00

ASEC Report ID : 77425
 Name of the Project : Cottages at Villa Rica - Rock Blasting
 Project Location : Villa Rica
 Weather : Cloudy
 Departure Time : 02/10/2025 17:00
 ASEC Technician Name : Micah Aycock

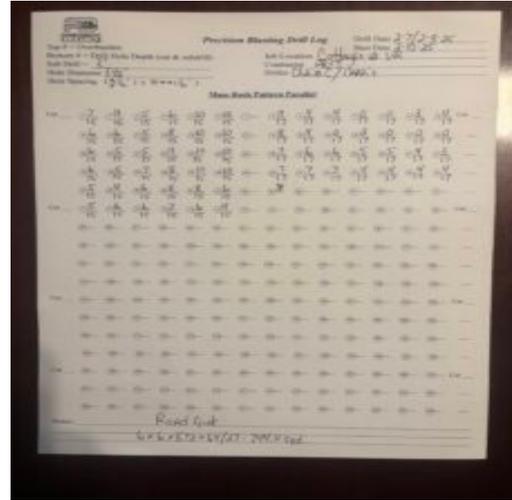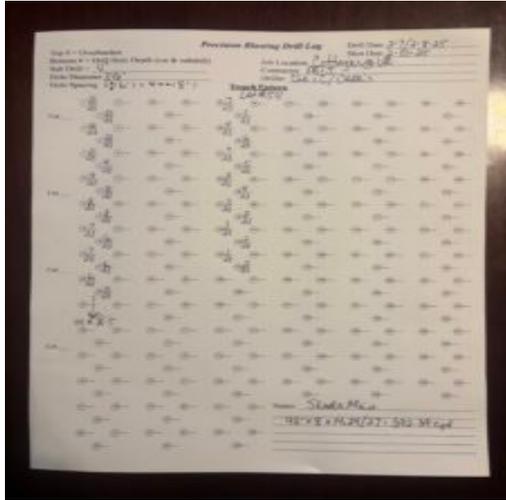

Ramchandra R. Mogulla
GA P.E. 036021
Senior Engineer

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
