

Date : 02/11/2025
Project No : 2024C315
Client Company : J. Chapman Const.
Arrival Time : 02/11/2025 13:30
Onsite Hours : 04:00

ASEC Report ID : 77440
Name of the Project : Cottages at Villa Rica - Rock Blasting
Project Location : Villa Rica
Weather : Rainy
Departure Time : 02/11/2025 17:30
ASEC Technician Name : Micah Aycock

The aforementioned AS Engineering and Consulting (ASEC) representative visited the Cottages at Villa Rica site to monitor drilling and rock removal operations. The contractor performing the work was Precision Blasting. The following observations were made on-site:

Drilling Data:




Because of the weather the precision blasting was only able to drill today. It continued south along the main sewer line where all the mass rock is located. The location was in-between lot #191 and lot #55. The pattern of the drilling still followed a trench in the middle and two mass rock patterns, one on each side of the trench. Progress was made but unfortunately, many of these holes will need to be cleaned out before the next blast, due to the weather.

We appreciate the opportunity to assist you with this project. Should you have any questions regarding this report, please do not hesitate to contact us. We would be happy to discuss it with you.



Date : 02/11/2025
 Project No : 2024C315
 Client Company : J. Chapman Const.
 Arrival Time : 02/11/2025 13:30
 Onsite Hours : 04:00

ASEC Report ID : 77440
 Name of the Project : Cottages at Villa Rica - Rock Blasting
 Project Location : Villa Rica
 Weather : Rainy
 Departure Time : 02/11/2025 17:30
 ASEC Technician Name : Micah Aycock

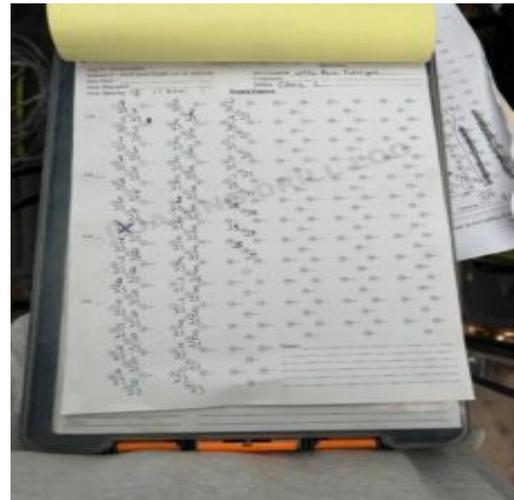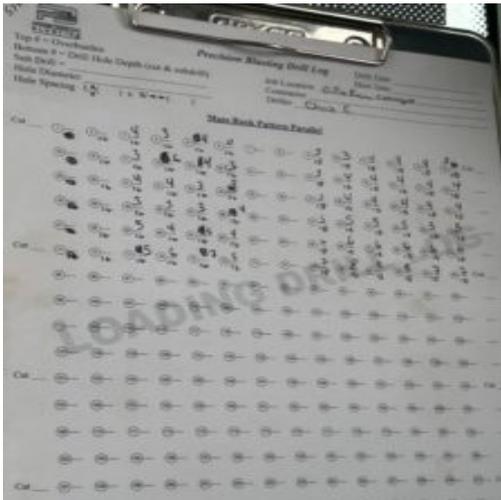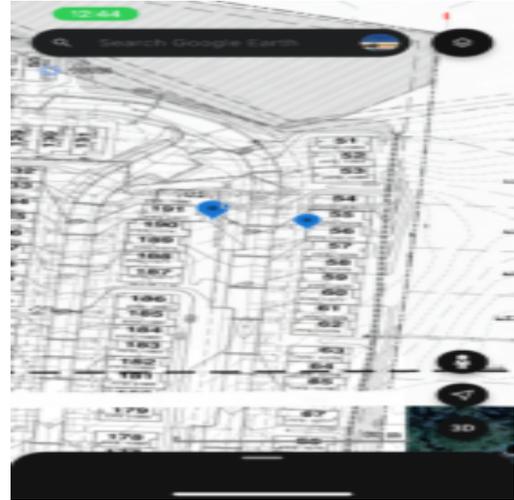

Ramchandra R. Mogulla
 GA P.E. 036021
 Senior Engineer

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
