

Date : 02/14/2025
Project No : 2024C315
Client Company : J. Chapman Const.
Arrival Time : 02/14/2025 10:00
Onsite Hours : 06:00

ASEC Report ID : 77449
Name of the Project : Cottages at Villa Rica - Rock Blasting
Project Location : Villa Rica
Weather : Sunny
Departure Time : 02/14/2025 16:00
ASEC Technician Name : Micah Aycock

The aforementioned AS Engineering and Consulting (ASEC) representative visited the Cottages at Villa Rica site to monitor drilling and rock removal operations. The contractor performing the work was Precision Blasting. The following observations were made on-site:

Drilling Data:



Because the weather cleared up today, precision blasting was able to continue drilling in preparation for the next blast. The drilling area followed the same pattern of trench in the center, with mass rock patterns on each side. The areas drilled were in-between lot #189/#188 and lot #57/#58. Good progress was made for next weeks blast, one driller was working on production drilling while the other was able to clean some previous drilling locations. Everything went according to plan and all drilling met with the production standards.

We appreciate the opportunity to assist you with this project. Should you have any questions regarding this report, please do not hesitate to contact us. We would be happy to discuss it with you.



Date : 02/14/2025
 Project No : 2024C315
 Client Company : J. Chapman Const.
 Arrival Time : 02/14/2025 10:00
 Onsite Hours : 06:00

ASEC Report ID : 77449
 Name of the Project : Cottages at Villa Rica - Rock Blasting
 Project Location : Villa Rica
 Weather : Sunny
 Departure Time : 02/14/2025 16:00
 ASEC Technician Name : Micah Aycock

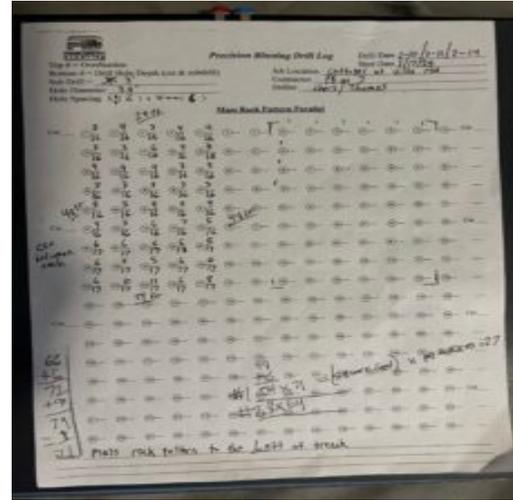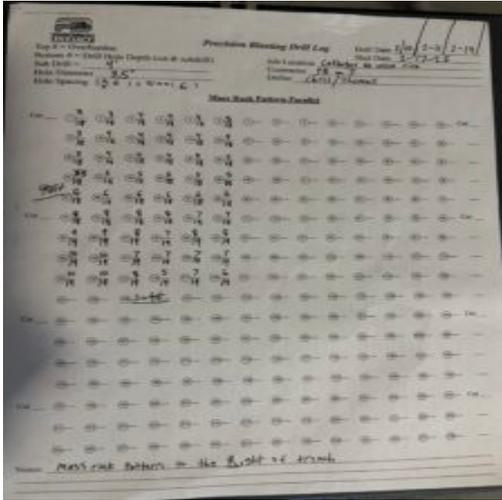

Ramchandra R. Mogulla
 GA P.E. 036021
 Senior Engineer

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
