

Date : 06/23/2025  
Project No : 2025C146  
Client Company : Davidson Homes, LLC  
Arrival Time : 06/23/2025 08:00  
Onsite Hours : 08:30

ASEC Report ID : 82512  
Name of the Project : Greene Farms Subdivision  
Project Location : 1451 Highway 113, Cartersville, Georgia  
Weather : Sunny  
Departure Time : 06/23/2025 16:30  
ASEC Technician Name : Clyde Smith

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.


Our representative was on site to observe the grading contractor undercut subgrade soils for the roadway between station 1+00 and 3+25 starting at building lot #87 removing saturated unsuitable soils to depths of approximately 3 feet and replacing with structural fill. The contractor placed the unsuitable undercut materials as fill for backyard Lots #87 thru #106 which was observed being placed in lifts bladed with a dozer but without any compactive efforts. The writer also observed the contractor placing structural fill for Lots #87 thru #106 which was placed in compacted lifts. Equipment observed onsite today were seventeen tandem dump trucks hauling in fill and two onsite off-road dump trucks with two 621 scrappers hauling soils onsite. The contractor also used two sheep-foot rollers compacting placed soils. The fill onsite was loaded using an excavator.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



Date : 06/23/2025  
Project No : 2025C146  
Client Company : Davidson Homes, LLC  
Arrival Time : 06/23/2025 08:00  
Onsite Hours : 08:30

ASEC Report ID : 82512  
Name of the Project : Greene Farms Subdivision  
Project Location : 1451 Highway 113, Cartersville, Georgia  
Weather : Sunny  
Departure Time : 06/23/2025 16:30  
ASEC Technician Name : Clyde Smith

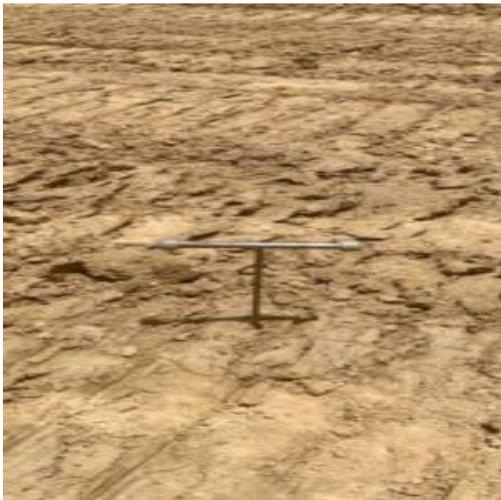

*Kenneth Mosman*

**Kenneth Mosman**

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
