


Date : 07/16/2025
Project No : 2025C146
Client Company : Davidson Homes, LLC
Arrival Time : 07/16/2025 08:00
Onsite Hours : 07:00

ASEC Report ID : 83031
Name of the Project : Greene Farms Subdivision
Project Location : 1451 Highway 113, Cartersville, Georgia
Weather :
Departure Time : 07/16/2025 15:00
ASEC Technician Name : Solomon Cherie

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Cutting and backfilling activities were continued this day. Hauling from within the cut area was carried out by the 845C dump trucks. Spreading was performed using a 61Pxi Komatsu dozer whereas cutting was performed by a 349E CAT excavator. Density testing included retests from previous day's failing tests were performed during grading operations.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

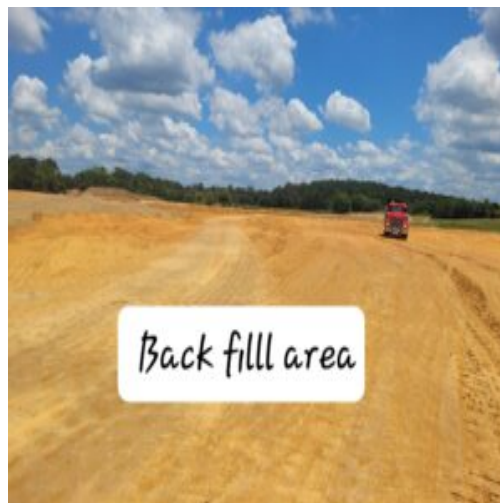

Picture depicting backfilled access road and building pad

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
