

Date : 07/25/2025
Project No : 2025C146
Client Company : Davidson Homes, LLC
Arrival Time : 07/25/2025 12:30
Onsite Hours : 03:30

ASEC Report ID : 83319
Name of the Project : Greene Farms Subdivision
Project Location : 1451 Highway 113, Cartersville, Georgia
Weather : sunny
Departure Time : 07/25/2025 16:00
ASEC Technician Name : Sean Willett


As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

On the above date, the technician was on site as requested by the contractor for observation/testing of soil.

The contractor requested compaction testing of the final grade on Lots #48 through #52. Test results showed approximately 95%-97% compaction in this general area. The technician recommended to compact this area one additional time with a vibrating sheep-foot roller. The contractor agreed.

The contractor continued placing topsoil along the greenspace located on these lots. Topsoil was placed in approximately 12in lifts and was compacted with a vibrating sheep's foot roller.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

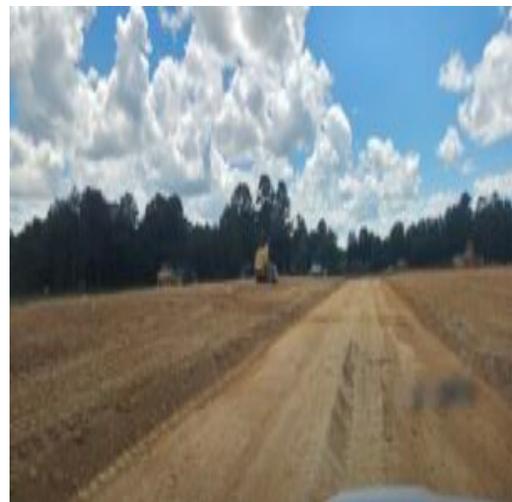

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
