


Date : 09/08/2025  
Project No : 2025C146  
Client Company : Davidson Homes, LLC  
Arrival Time : 09/08/2025 10:00  
Onsite Hours : 06:00

ASEC Report ID : 85306  
Name of the Project : Greene Farms Subdivision  
Project Location : 1451 Highway 113, Cartersville, Georgia  
Weather : N/A  
Departure Time : 09/08/2025 16:00  
ASEC Technician Name : Solomon Cherie

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Our ASEC representative was on site as requested and observed the grading contractor continue placing fill for the building pads Lots #53 through #67. The contractor continued to scarify and aerate wet soils and are replacing fill areas as soils approach optimum moisture content. Density tests were performed using a Troxler nuclear gauge model 3430, serial no. 38069. Results are attached.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

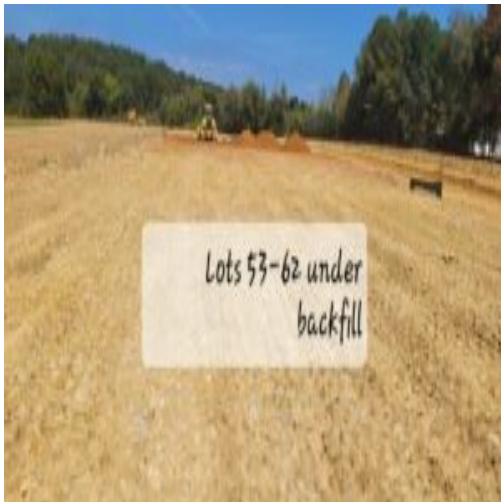

Picture depicting lots#53-62 backfilled and tested and have pretty good compaction



Above pic showed Lots#62-67 being ploughed to be scarified and repacked

*Kenneth Mosman*

**Kenneth Mosman**

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
