

Date : 04/01/2025  
Project No : 2025C150  
Client Company : Davidson Homes  
Arrival Time : 04/01/2025 08:00  
Onsite Hours : 08:30

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Work has continued behind Lots #225, #226, and #227. The contractor has made progress in the preparation of the retaining wall foundation.


Excavation was carried out using a Kobelco SK210H. The geo-grid has been installed across the excavated area, providing reinforcement for the subsequent stages of the retaining wall construction. On top of the geo-grid, a fiber sheet has been applied. Additionally, a granular stone base has been placed on top of the fiber sheet for additional stability, preparing the area for the next phases of construction. Lot #227 has a sewer line integrated into the retaining wall structure. The pipe has been excavated and installed at a depth below the stone grade cut level, specifically positioned 4 feet below the top of the retaining wall.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.




ASEC Report ID : 79495  
Name of the Project : Riverwood Retaining Wall  
Project Location : Dallas  
Weather : sunny  
Departure Time : 04/01/2025 16:30  
ASEC Technician Name : Vamsi Polisetty

Date : 04/01/2025  
Project No : 2025C150  
Client Company : Davidson Homes  
Arrival Time : 04/01/2025 08:00  
Onsite Hours : 08:30

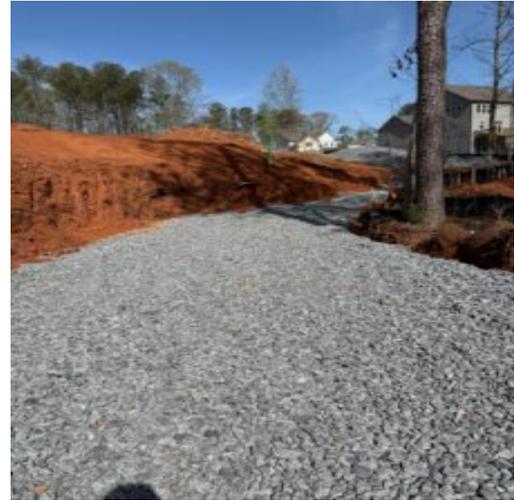

Date : 04/01/2025  
Project No : 2025C150  
Client Company : Davidson Homes  
Arrival Time : 04/01/2025 08:00  
Onsite Hours : 08:30

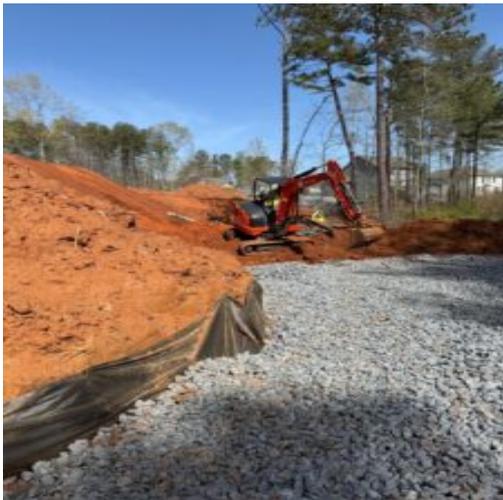

ASEC Report ID : 79495  
Name of the Project : Riverwood Retaining Wall  
Project Location : Dallas  
Weather : sunny  
Departure Time : 04/01/2025 16:30  
ASEC Technician Name : Vamsi Polisetty

Date : 04/01/2025  
Project No : 2025C150  
Client Company : Davidson Homes  
Arrival Time : 04/01/2025 08:00  
Onsite Hours : 08:30



*Kenneth Mosman*

**Kenneth Mosman**

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
