

Date : 04/25/2025
Project No : 2025C160
Client Company : Artisan
Arrival Time : 04/25/2025 9:30
Onsite Hours : 06:30

ASEC Report ID : 81687
Name of the Project : Rockmart Township - 115 Felton Drive
Project Location : Rockmart
Weather : cloudy
Departure Time : 04/25/2025 16:00
ASEC Technician Name : Aminullah Azimi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.


- The placement and compaction of fill for Lots #116, #117, #118, #119, #120, #121 continued today. A soil sample was retrieved and returned to our laboratory to perform a moisture-density relationship (proctor).
- At the time of arrival, our representative observed that work was in progress with 1-foot lifts being placed and compacted using 815 compaction equipment. Compaction testing was performed using a Troxler nuclear density gauge of Soil (ASTM D 2937), along with general probing using a 3/8" diameter probe rod.
- Density test results indicate that the compacted materials met the project requirement of 95% of the maximum dry density obtained by a Standard Proctor ASTM 698.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



Date : 04/25/2025
Project No : 2025C160
Client Company : Artisan
Arrival Time : 04/25/2025 9:30
Onsite Hours : 06:30

ASEC Report ID : 81687
Name of the Project : Rockmart Township - 115 Felton Drive
Project Location : Rockmart
Weather : cloudy
Departure Time : 04/25/2025 16:00
ASEC Technician Name : Aminullah Azimi

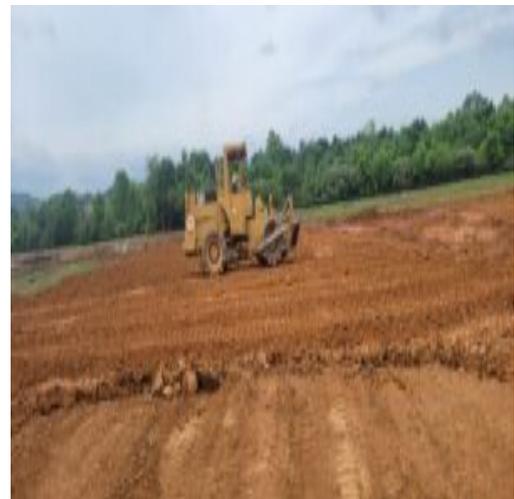

Date : 04/25/2025
Project No : 2025C160
Client Company : Artisan
Arrival Time : 04/25/2025 9:30
Onsite Hours : 06:30

ASEC Report ID : 81687
Name of the Project : Rockmart Township - 115 Felton Drive
Project Location : Rockmart
Weather : cloudy
Departure Time : 04/25/2025 16:00
ASEC Technician Name : Aminullah Azimi



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
