

Date : 06/09/2025
Project No : 2025C160
Client Company : Artisan
Arrival Time : 06/09/2025 08:30
Onsite Hours : 03:00

ASEC Report ID : 82119
Name of the Project : Rockmart Township - 115 Felton Drive
Project Location : Rockmart
Weather : sunny
Departure Time : 06/09/2025 11:30
ASEC Technician Name : Sean Willett

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.


Our ASEC representative was on site as requested by the contractor (Wilbanks) for the observation/testing of the placement of fill/backfill. The technician observed the contractor place 1 lift approximately 8 inches in thickness over Lots #5 through #13. The fill was placed in approx. 8-to-12-inch lifts. Only 1 lift was placed. The contractor stripped and placed topsoil on the bank in the backyards (greenspace) of these lots.

The contractor continued excavation/installation of SSMH 4.3 with a reported undercut of approximately 2 feet, bedded with No. 57 to elevation.

The contractor continued work on BE6, installed with RCP, with an invert elevation of 753.2.

The site was shut down early due to rain around lunchtime.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

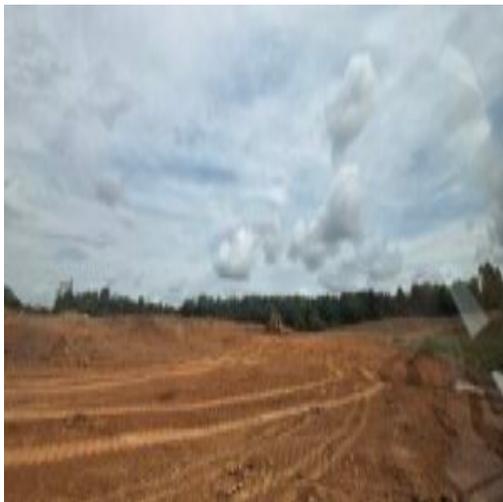

Date : 06/09/2025
Project No : 2025C160
Client Company : Artisan
Arrival Time : 06/09/2025 08:30
Onsite Hours : 03:00

ASEC Report ID : 82119
Name of the Project : Rockmart Township - 115 Felton Drive
Project Location : Rockmart
Weather : sunny
Departure Time : 06/09/2025 11:30
ASEC Technician Name : Sean Willett



Date : 06/09/2025
Project No : 2025C160
Client Company : Artisan
Arrival Time : 06/09/2025 08:30
Onsite Hours : 03:00

ASEC Report ID : 82119
Name of the Project : Rockmart Township - 115 Felton Drive
Project Location : Rockmart
Weather : sunny
Departure Time : 06/09/2025 11:30
ASEC Technician Name : Sean Willett



Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
