

Date : 07/18/2025  
Project No : 2025C160  
Client Company : Artisan  
Arrival Time : 07/18/2025 08:30  
Onsite Hours : 04:30

ASEC Report ID : 83137  
Name of the Project : Rockmart Township - 115 Felton Drive  
Project Location : Rockmart  
Weather : overcast  
Departure Time : 07/18/2025 13:00  
ASEC Technician Name : Sean Willett

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Our ASEC representative was on site as requested by the contractor (Wilbanks) for the observation/testing of the placement of fill/backfill. Our representative observed the contractor placing lifts approximately 8 inches in thickness over Lots #72 through #78.

The contractor built up the slope easement between Lot #209 and Lot #64. During this time, the contractor hit what appeared to be either a phone line or fiber optic line buried in the ground in this area. The contractor is actively working to get this fixed. They are not positive if the line is active or not.


Our representative density tested Lots #166 through #168. Many of the tests did not meet job specifications for compaction. Test results were provided to the contractor and it was recommended to add some moisture back into the in-situ soils prior to compaction.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



Date : 07/18/2025  
Project No : 2025C160  
Client Company : Artisan  
Arrival Time : 07/18/2025 08:30  
Onsite Hours : 04:30

ASEC Report ID : 83137  
Name of the Project : Rockmart Township - 115 Felton Drive  
Project Location : Rockmart  
Weather : overcast  
Departure Time : 07/18/2025 13:00  
ASEC Technician Name : Sean Willett

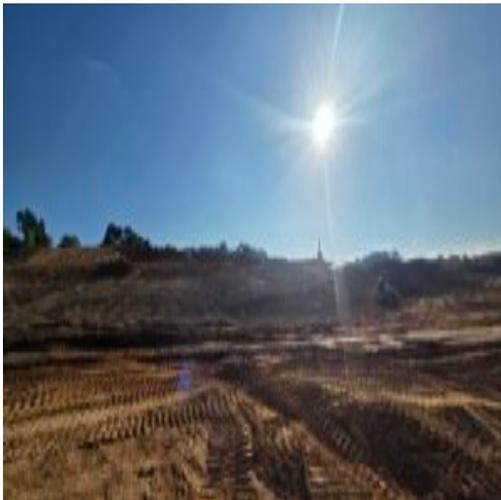

*Kenneth Mosman*

**Kenneth Mosman**

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
