

Date : 07/25/2025
Project No : 2025C160
Client Company : Artisan
Arrival Time : 07/25/2025 07:00
Onsite Hours : 05:00

ASEC Report ID : 83315
Name of the Project : Rockmart Township - 115 Felton Drive
Project Location : Rockmart
Weather : sunny
Departure Time : 07/25/2025 12:00
ASEC Technician Name : Sean Willett


As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Our ASEC representative was on site as requested by the contractor (Wilbanks) for the observation/testing of the placement of fill/backfill. The technician and contractor conducted a proof roll of Lots #53 through #60. Lots #50 through #52 contain a temporary retention pond that appeared to be wet from the previous night's rain. The technician and contractor agreed to let this area aerate over the weekend before attempting a proof-roll. All low compaction areas were cut until well compacted ground was present.

The contractor then began placing fill across these lots in approximate 8 to 12 inches of thickness and compacting via sheep-foot roller.

The contractor started cutting out roadways between Lots #208 and #224 areas.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

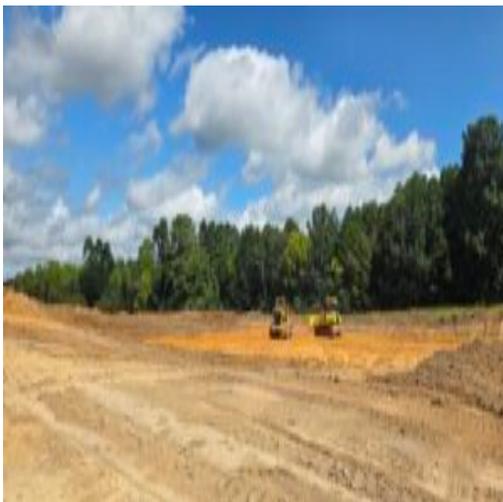

proof roll

Date : 07/25/2025
Project No : 2025C160
Client Company : Artisan
Arrival Time : 07/25/2025 07:00
Onsite Hours : 05:00

ASEC Report ID : 83315
Name of the Project : Rockmart Township - 115 Felton Drive
Project Location : Rockmart
Weather : sunny
Departure Time : 07/25/2025 12:00
ASEC Technician Name : Sean Willett



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
