

Date : 11/12/2025
Project No : 2025C211
Client Company : Pulte
Arrival Time : 11/12/2025 07:30
Onsite Hours : 07:30

ASEC Report ID : 87797
Name of the Project : Haley's Bluff - Philadelphia Rd.
Project Location : Jasper
Weather : Sunny
Departure Time : 11/12/2025 15:00
ASEC Technician Name : Sean Willett

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Our ASEC representative was on site for the observation/testing of the placement of fill/backfill. The contractor continued placing fill on Lots #1 through #4 in approximately 6 inch to 8 inch lifts. The lifts were compacted using an 815 sheeps-foot roller and a smaller HAMM vibrating sheep's foot roller. As the contractor works up the natural slope, they are benching out the slope approximately every 1 foot to 2 feet. ASEC performed density testing on the lots and roadway in front of the lots. All failed tests were addressed, and all test results were provided to the contractor. A field proctor was performed on the fill being excavated from the commercial lot area above the Connex (at the entrance of site). The soil appeared to be a dark red silty soil with a large amount of mica present. The remaining stockpiled topsoil was moved to the slope of the front detention pond. The topsoil was spread and rolled in along the slope using a dozer.

The contractor began excavation of a new horizontal boring location by the front entrance to the site. The contractor exposed the gas main and water main by shovel and then excavated the remaining area. The boring is going under Philadelphia Road (near the entrance to the new gas station on the corner of Philadelphia and Hwy 575).

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



front detention pond



lot #1 area

Date : 11/12/2025
Project No : 2025C211
Client Company : Pulte
Arrival Time : 11/12/2025 07:30
Onsite Hours : 07:30

ASEC Report ID : 87797
Name of the Project : Haley's Bluff - Philadelphia Rd.
Project Location : Jasper
Weather : Sunny
Departure Time : 11/12/2025 15:00
ASEC Technician Name : Sean Willett




boring



boring



lot #1 - #4 area

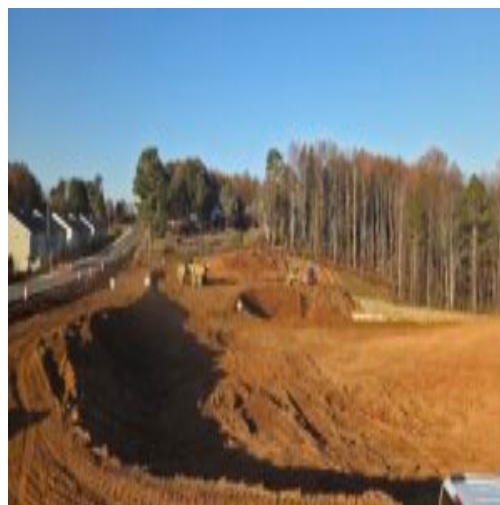

lot #1 - #4 area

Date : 11/12/2025
Project No : 2025C211
Client Company : Pulte
Arrival Time : 11/12/2025 07:30
Onsite Hours : 07:30

ASEC Report ID : 87797
Name of the Project : Haley's Bluff - Philadelphia Rd.
Project Location : Jasper
Weather : Sunny
Departure Time : 11/12/2025 15:00
ASEC Technician Name : Sean Willett



front detention pond



lot #1 - #4 area



water main on Philadelphia road

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
