

Date : 04/21/2026
Project No : 2025C211
Client Company : Pulte
Arrival Time : 04/21/2026 11:00
Onsite Hours : 01:00


ASEC Report ID : 93301
Name of the Project : Haley's Bluff - Philadelphia Rd.
Project Location : Jasper
Weather : Sunny
Departure Time : 04/21/2026 12:00
ASEC Technician Name : Sean Willett

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Our ASEC representative was on site to observe the contractor (NG Grading) and for the observation/testing of the placement of fill/backfill. The grading crew is continuing to place blasted rock lifts across the Lots #33 through #44 located above retaining wall 1. ASEC watched as loaded off road trucks rolled across the lifts to check for stability. There does not appear to be any severe pumping or deflection present.

DCP Testing/inspection was requested for the base of the pump station located by the back pond. The contractors are using a chipping hammer attachment on an excavator to remove hard rock from this area. It appears the whole foundation of the pump station will be placed on this hard rock. Please see photos below.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

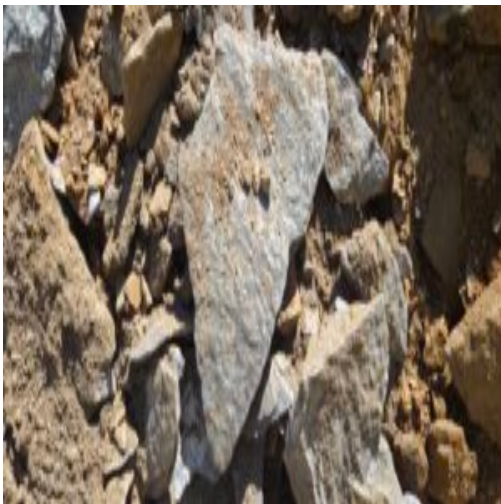

rock removed from pump station



pump station foundation/footing

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
