

Date : 10/13/2025  
Project No : 2025C216  
Client Company : Artisan  
Arrival Time : 10/13/2025 11:30  
Onsite Hours : 04:00

ASEC Report ID : 86821  
Name of the Project : NW (Lots) Unit 4 PH 1A & 1B  
Project Location : Dallas  
Weather : Sunny  
Departure Time : 10/13/2025 15:30  
ASEC Technician Name : Clyde Smith

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

On the above date our representative was on site to observe the grading contractor continue placing fill for building Lot #18 and complete subgrade prep at building Lots #12 thru #17 by proof-rolling the lots using a loaded off-road dump truck making two passes over all areas. The subgrade soils appeared stable under traffic and was approved for continued fill placement.

The Erosion contractor (Valor) continued grassing building lots.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.




Proof rolling building lots



Date : 10/13/2025  
Project No : 2025C216  
Client Company : Artisan  
Arrival Time : 10/13/2025 11:30  
Onsite Hours : 04:00

ASEC Report ID : 86821  
Name of the Project : NW (Lots) Unit 4 PH 1A & 1B  
Project Location : Dallas  
Weather : Sunny  
Departure Time : 10/13/2025 15:30  
ASEC Technician Name : Clyde Smith

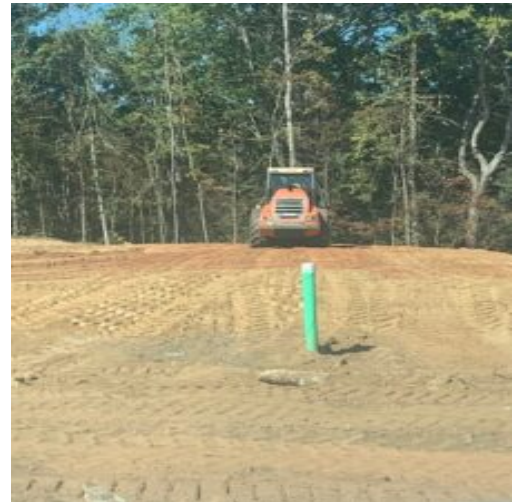


Fill placement at building lot#18



Slope matting

Date : 10/13/2025  
Project No : 2025C216  
Client Company : Artisan  
Arrival Time : 10/13/2025 11:30  
Onsite Hours : 04:00

ASEC Report ID : 86821  
Name of the Project : NW (Lots) Unit 4 PH 1A & 1B  
Project Location : Dallas  
Weather : Sunny  
Departure Time : 10/13/2025 15:30  
ASEC Technician Name : Clyde Smith

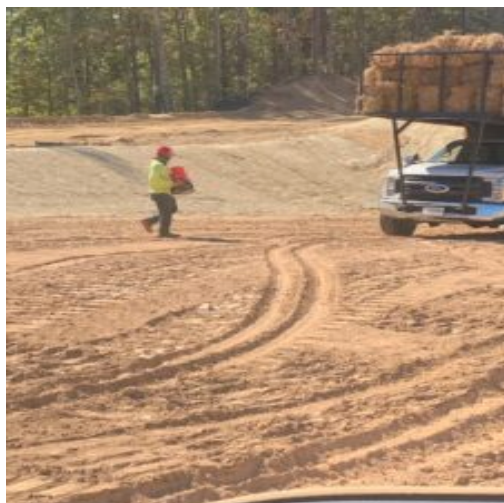

Erosion seeding



Drilling log

*Kenneth Mosman*

**Kenneth Mosman**

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
