

Date : 10/24/2025
Project No : 2025C244
Client Company : McCallan Group
Arrival Time : 10/24/2025 07:30
Onsite Hours : 9:30

ASEC Report ID : 87399
Name of the Project : Cassville Rd tract, proposed Burrito
Wrap
Project Location : Cartersville
Weather : sunny
Departure Time : 10/24/2025 17:00
ASEC Technician Name : Samara Simha Reddy Kandi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Proof-rolling was performed at Stations ST-A7 and ST-A5 using a fully loaded tandem-axled dump truck. Multiple passes, both forward and backward, over the designated areas was performed to evaluate stability of the subgrade. Subgrade soils displayed no signs of movement, rutting, pumping, or deflection.


Following successful proof-rolling, the crew proceeded with fill placement and compaction. A total of approximately 20 inches of fill was placed in three successive lifts, each lift measuring about 6 to 7 inches in thickness. Each lift was uniformly spread, moisture-conditioned, and compacted.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



Date : 10/24/2025
Project No : 2025C244
Client Company : McCallan Group
Arrival Time : 10/24/2025 07:30
Onsite Hours : 9:30

ASEC Report ID : 87399
Name of the Project : Cassville Rd tract, proposed Burrito
Wrap
Project Location : Cartersville
Weather : sunny
Departure Time : 10/24/2025 17:00
ASEC Technician Name : Samara Simha Reddy Kandi

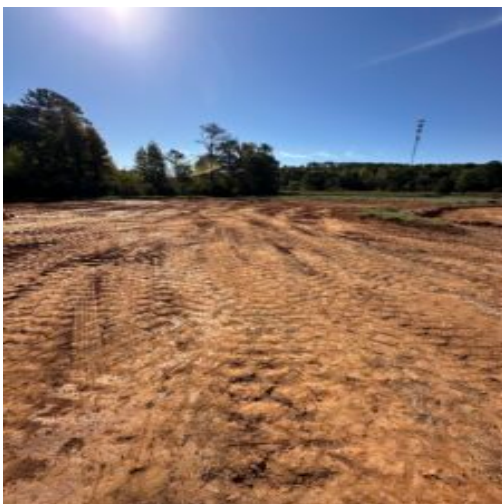

Date : 10/24/2025
Project No : 2025C244
Client Company : McCallan Group
Arrival Time : 10/24/2025 07:30
Onsite Hours : 9:30

ASEC Report ID : 87399
Name of the Project : Cassville Rd tract, proposed Burrito
Wrap
Project Location : Cartersville
Weather : sunny
Departure Time : 10/24/2025 17:00
ASEC Technician Name : Samara Simha Reddy Kandi



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
