

Date : 10/30/2025
Project No : 2025C244
Client Company : McCallan Group
Arrival Time : 10/30/2025 07:30
Onsite Hours : 10:30

ASEC Report ID : 87418
Name of the Project : Cassville Rd tract, proposed Burrito
Wrap
Project Location : Cartersville
Weather : cloudy
Departure Time : 10/30/2025 18:00
ASEC Technician Name : Samara Simha Reddy Kandi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Excavation and installation continued today at the Cassville Road tract for the French drain ("burrito wrap") project. Work continued at Point B4, where the crew excavated the area to the required depth, installed the new drainage pipes, and performed backfilling operations. The excavated soil was replaced in lifts and compacted.


After completing work at Point B4, the crew moved to Point C3 (midway section) as indicated in the revised construction plan. The site was cleared of debris and loose material before excavation. Excavation was then carried out to the design grade, and pipes were installed and backfilled in controlled lifts and compacted. No groundwater was observed at the time of excavation.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



Date : 10/30/2025
Project No : 2025C244
Client Company : McCallan Group
Arrival Time : 10/30/2025 07:30
Onsite Hours : 10:30

ASEC Report ID : 87418
Name of the Project : Cassville Rd tract, proposed Burrito
Wrap
Project Location : Cartersville
Weather : cloudy
Departure Time : 10/30/2025 18:00
ASEC Technician Name : Samara Simha Reddy Kandi

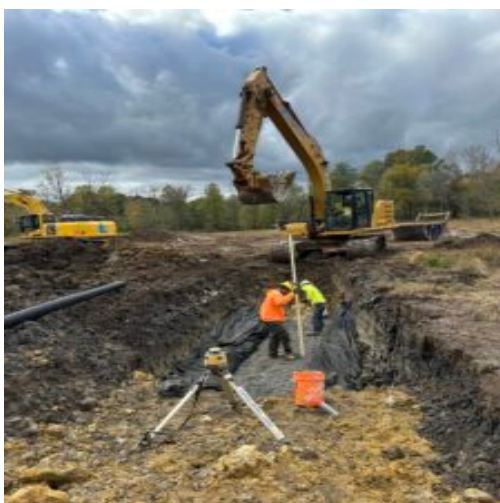

Date : 10/30/2025
Project No : 2025C244
Client Company : McCallan Group
Arrival Time : 10/30/2025 07:30
Onsite Hours : 10:30

ASEC Report ID : 87418
Name of the Project : Cassville Rd tract, proposed Burrito
Wrap
Project Location : Cartersville
Weather : cloudy
Departure Time : 10/30/2025 18:00
ASEC Technician Name : Samara Simha Reddy Kandi



Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
