

Date : 11/20/2025  
Project No : 2025C244  
Client Company : McCallan Group  
Arrival Time : 11/20/2025 07:30  
Onsite Hours : 11:00

ASEC Report ID : 88175  
Name of the Project : Cassville Rd tract, proposed Burrito  
Wrap  
Project Location : Cartersville  
Weather : sunny  
Departure Time : 11/20/2025 18:30  
ASEC Technician Name : Samara Simha Reddy Kand

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

The crew continued working at SD3-A, installing the drainage access as per the plan in the north direction and leveling the area. They also placed riprap at four locations.

At SD3-B, the crew installed the drainage access in the northeast direction, leveled the area, and placed three riprap sections as per the plan.

Stockpiled soil was then placed between Buildings #15 through #19 in two lifts, and each lift was compacted.


Meanwhile, the erosion-control crew continued installing straw erosion control blankets along the SD3-A pond slopes.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.



Date : 11/20/2025  
Project No : 2025C244  
Client Company : McCallan Group  
Arrival Time : 11/20/2025 07:30  
Onsite Hours : 11:00

ASEC Report ID : 88175  
Name of the Project : Cassville Rd tract, proposed Burrito  
Wrap  
Project Location : Cartersville  
Weather : sunny  
Departure Time : 11/20/2025 18:30  
ASEC Technician Name : Samara Simha Reddy Kandi

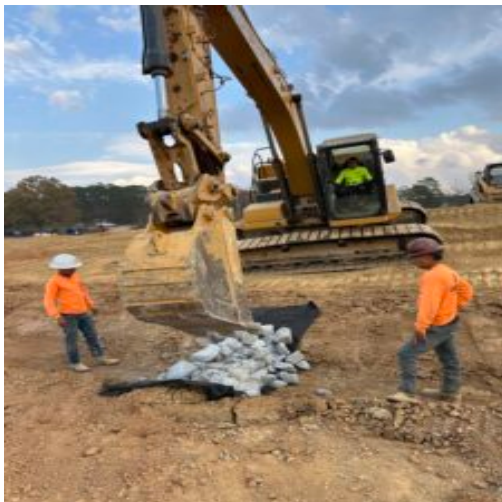

Date : 11/20/2025  
Project No : 2025C244  
Client Company : McCallan Group  
Arrival Time : 11/20/2025 07:30  
Onsite Hours : 11:00

ASEC Report ID : 88175  
Name of the Project : Cassville Rd tract, proposed Burrito  
Wrap  
Project Location : Cartersville  
Weather : sunny  
Departure Time : 11/20/2025 18:30  
ASEC Technician Name : Samara Simha Reddy Kandi



*Kenneth Mosman*

**Kenneth Mosman**

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
