



Date : 11/24/2025
Project No : 2025C244
Client Company : McCallan Group
Arrival Time : 11/24/2025 07:30
Onsite Hours : 11:00

ASEC Report ID : 88199
Name of the Project : Cassville Rd tract, proposed Burrito
Wrap
Project Location : Cartersville
Weather : cloudy
Departure Time : 11/24/2025 18:30
ASEC Technician Name : Samara Simha Reddy Kandi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

Work began with draining water from the ponds to allow grading activities to continue. After dewatering, all soil stockpiles across the site were moved and consolidated to one side. The crew then worked on grading and shaping the slopes to the required elevations. Once the slopes were trimmed, the ground surface was leveled across the working area. Final smoothing was completed followed by compaction.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you

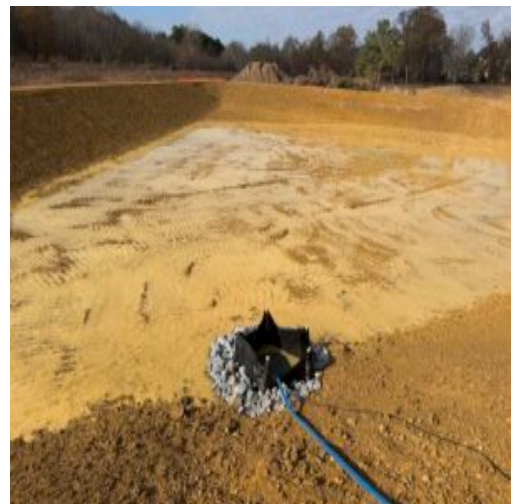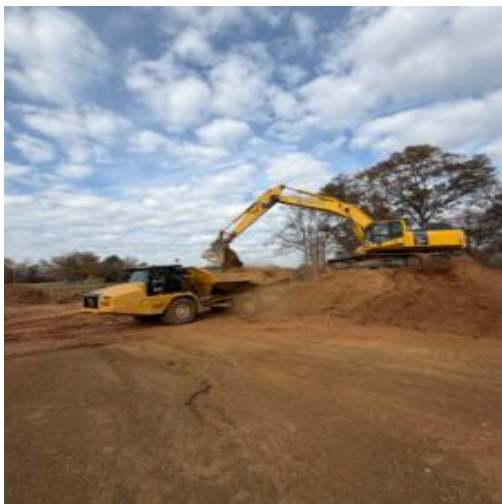

Date : 11/24/2025
Project No : 2025C244
Client Company : McCallan Group
Arrival Time : 11/24/2025 07:30
Onsite Hours : 11:00

ASEC Report ID : 88199
Name of the Project : Cassville Rd tract, proposed Burrito
Wrap
Project Location : Cartersville
Weather : cloudy
Departure Time : 11/24/2025 18:30
ASEC Technician Name : Samara Simha Reddy Kandi



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
