

Date : 01/07/2026
Project No : 2025C244
Client Company : McCallan Group
Arrival Time : 01/07/2026 07:45
Onsite Hours : 10:15


ASEC Report ID : 89090
Name of the Project : Cassville Rd tract, proposed Burrito
Wrap
Project Location : Cartersville
Weather : cloudy
Departure Time : 01/07/2026 18:00
ASEC Technician Name : Samara Simha Reddy Kandi

As requested, the site was visited by our AS Engineering and Consulting (ASEC) representative for the purpose of providing quality control inspection and testing services. Visual observation techniques were employed to verify compliance with project drawing/specifications, applicable codes, and materials submittals. The following observations were observed on site this day.

The crew continued earthwork and pond restoration activities at Pond 1. The pond was drained, and excavation operations were performed to remove saturated and unsuitable soils from the pond bottom and surrounding areas. Excavated material was hauled and redistributed to Lots #89 through 96 for fill operations. At Lots #89 through 96, fill material was placed in controlled lifts of approximately 6-8 inches. Each lift was moisture-conditioned and compacted.

A proof-roll was performed between Lots #85 and 88, and the subgrade was found to be suitable for fill placement. No severe yielding, rutting, or instability was observed during proof-rolling. Following approval, additional fill lifts were placed and compacted.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

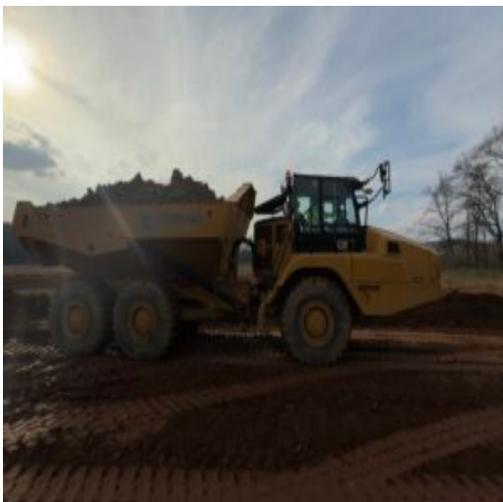

Date : 01/07/2026
Project No : 2025C244
Client Company : McCallan Group
Arrival Time : 01/07/2026 07:45
Onsite Hours : 10:15

ASEC Report ID : 89090
Name of the Project : Cassville Rd tract, proposed Burrito
Wrap
Project Location : Cartersville
Weather : cloudy
Departure Time : 01/07/2026 18:00
ASEC Technician Name : Samara Simha Reddy Kandi



Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
