

Date : 03/09/2026  
Project No : 2026C103  
Client Company : Artisan  
Arrival Time : 03/09/2026 08:00  
Onsite Hours : 9:00

ASEC Report ID : 91136  
Name of the Project : NW PH 2, UNIT 4  
Project Location : Dallas  
Weather : sunny  
Departure Time : 03/09/2026 17:00  
ASEC Technician Name : Clyde Smith

On the above date the writer was onsite as requested and observed the Pipe contractor continue installing 8" ductile iron sanitary sewer line between manhole structures #7 and 8. The writer observed backfilling at deep elevations which was placed and compacted in suitable lifts. The contractor had installed sanitary sewer line from halfway between manhole # 4 and 5, also from #5 thru 7 on 3/7/26 without the writer present onsite.


The Grading contractor continued placing rock fill at building lots# 33 thru 36 that was monitored by the writer at elevation 902. The observed rock fill placement was suitable for site specifications.

The Blast contractor (Advance) made a blast shot today at lots# 45 and 46. The blast drill log is attached.



Date : 03/09/2026  
Project No : 2026C103  
Client Company : Artisan  
Arrival Time : 03/09/2026 08:00  
Onsite Hours : 9:00

ASEC Report ID : 91136  
Name of the Project : NW PH 2, UNIT 4  
Project Location : Dallas  
Weather : sunny  
Departure Time : 03/09/2026 17:00  
ASEC Technician Name : Clyde Smith

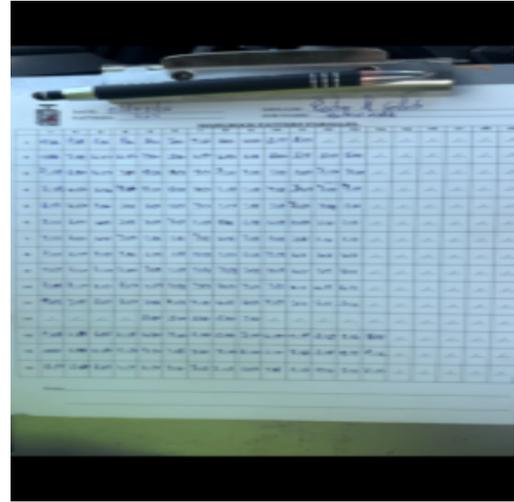

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
