


Date : 12/13/2024
Project No : 2024C223
Client Company : CWM
Arrival Time : 12/13/2024 6:45
Onsite Hours : 03:15

ASEC Report ID : 74445
Name of the Project : Concourse E Gate & Ramp 6 North Gate
Project Location : HJAIA
Weather : sunny
Departure Time : 12/13/2024 10:
ASEC Technician Name : Aminullah Azimi

As requested, our AS Engineering & Consulting LLC representative was on site observe the placement of concrete for Location L24.

The undersigned arrived on-site to observe the placement of 70 cubic yards of low-slump concrete at Concourse E, location L24. The following test result details were recorded:

- **Slump:** 3.25 inches
- **Air Temperature:** 42°F
- **Maximum Concrete Temperature:** 58°F
- **Unit Weight:** 141.4 pounds per cubic foot
- **Air Content:** 4.5%

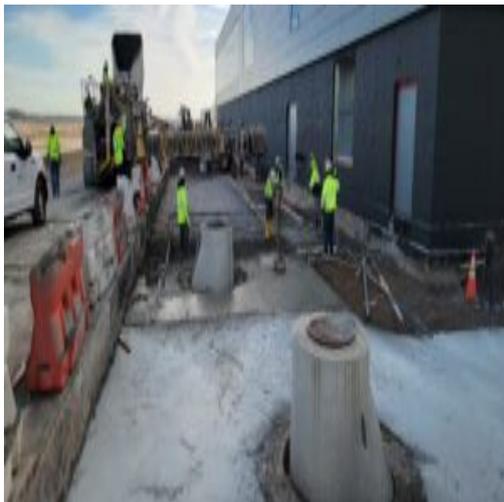

Kenneth Mosman

Kenneth Mosman

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
