

Date : 04/17/2026
Project No : 2025C211
Client Company : Pulte
Arrival Time :
Onsite Hours : N/A

ASEC Report ID : 92978
Name of the Project : Haley's Bluff - Philadelphia Rd.
Project Location : Jasper
Weather : N/A
Departure Time :
ASEC Technician Name : Kenneth Mosman



As requested, AS Engineering and Consulting (ASEC) has completed a verification of the rock quantity amounts determined by Elevate Drilling & Blasting LLC on March 18 and 19 (and referred to as Blast #5).

Rock volume was determined based on the attached drill logs. Drilling was performed on **March 18 and 19, 2026**. Based on information provided by the contractor, a grid spacing of 8 feet was used. A total of 129 holes were drilled (88 on March 18 and 41 on March 19).

The total quantity of mass rock shot on these days was calculated to be approximately **2488.89 cubic yards**.


Also attached is a sketch of the approximate location for Blast #5. The green areas depicted refer to the drilling performed on March 18 and 19. The yellow area was an area previously drilled on February 17, 2026, that was drilled for exploratory purposes only.

We appreciate the opportunity to be of service to you on this project. If you have any questions regarding this report, please feel free to contact us. We will be more than happy to discuss it with you.

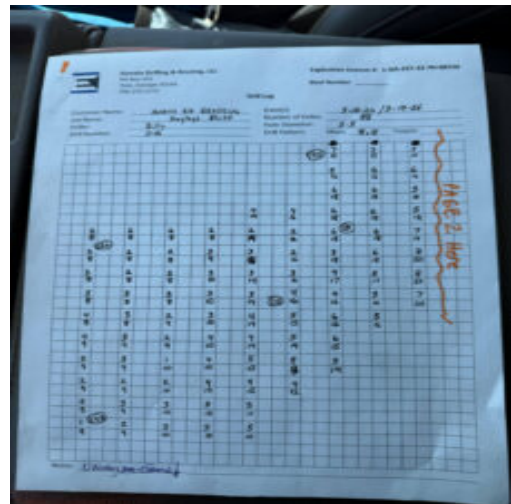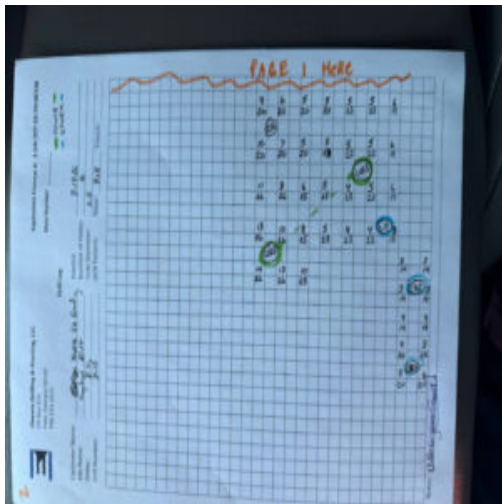

Date : 04/17/2026
Project No : 2025C211
Client Company : Pulte
Arrival Time :
Onsite Hours : N/A

ASEC Report ID : 92978
Name of the Project : Haley's Bluff - Philadelphia Rd.
Project Location : Jasper
Weather : N/A
Departure Time :
ASEC Technician Name : Kenneth Mosman

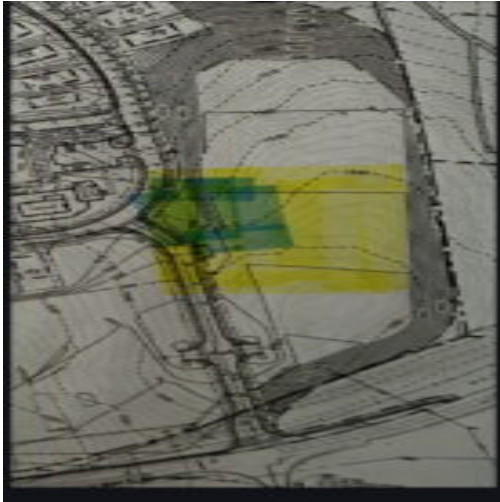

Kenneth Mosman

Kenneth Mosman
Project Professional

The results presented in this report relate only to the items tested. This report shall not be reproduced, except in full, without written approval from AS Engineering and Consulting LLC.
